



Daily Logs List

Jul 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Whitcomb Plumbing
Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

-Unloaded equipment on the south side grounds

-Will soon be correcting the mistake of tying the gas line to the sprinkler system

Weather Conditions:

Partly cloudy with isolated storms Wed, Jul 22, 2026, 7:01 AM



91°F

Wind: 13 mph

62°F

Humidity: 72%

Total Precip: 0.02"

Attachments: 0

Jul 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 3:35

-Opened site: unlocked upper main and south side door, lower level door, job box, turned on power, and completed a perimeter sweep

-Maintaining site

Weather Conditions:

Partly cloudy with isolated showers Wed, Jul 22, 2026, 6:48 AM



89°F

Wind: 11 mph

65°F

Humidity: 68%

Total Precip: 0.06"

Attachments: 0

Jul 21, 2026

Job: 2927 W Pikes Peak Ave
Title: Summit Fire
Added By: Marlowe Downey

Log Notes:

Arrived at 8:50

- Unloaded tools and equipment in the upper level
- Continuing runs in the hallway as well as the sanctuary
- Cleaned up areas worked in

Left at 3:50

Weather Conditions:

Partly cloudy with showers Tue, Jul 21, 2026, 9:15 AM



91°F

65°F

Wind: 15 mph

Humidity: 60%

Total Precip: 0.01"

Attachments: 0

Jul 21, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:15

- Wrapping up work in the sanctuary by installing 90 degree ducting stub outs
- Will be starting roof pop outs after sanctuary completion

Left at 3:40

Weather Conditions:

Partly cloudy with showers Tue, Jul 21, 2026, 9:15 AM



91°F

65°F

Wind: 15 mph

Humidity: 60%

Total Precip: 0.01"

Attachments: 1



Jul 21, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:50

- Opened site: unlocked upper main and south side door, lower level door, job box, turned on power, and completed a perimeter sweep
- Took trash out
- Put equipment away and organized material from yesterdays work
- Assisting and supervising CWAM
- Assisting and supervising Summit Fire

- Assisting and supervising Ownership Team
- Measured and marked out stairwell railing for Ownership Team
- Ownership Team cut blocking for stairway (waiting to install upon confirmation of hardware size), reduced chase size in lower level bathroom 109 for sprinkler head code
- Cleaned up work areas from trades
- Went over site progress with the trades

Left at 4:00

Weather Conditions:

Partly cloudy with showers Tue, Jul 21, 2026, 7:15 AM



93°F

68°F

Wind: 20 mph

Humidity: 54%

Total Precip: 0.13"

Attachments: 4



Jul 20, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 7:45

- Set up tools and equipment in upper level
- Continued vertical runs in upper level and preparing for stub outs
- Completed runs in upper level rooms 202, 202A, 203A, 203

Left at 3:45

Weather Conditions:

Mostly sunny Mon, Jul 20, 2026, 9:59 AM



97°F

62°F

Wind: 10 mph

Humidity: 63%

Total Precip: 0"

Attachments: 2



Jul 20, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

- Set up tools and equipment in upper level
- Worked on drip pans and condensation lines on all furnaces

Left at 3:30

Weather Conditions:

Mostly sunny Mon, Jul 20, 2026, 9:59 AM



97°F

62°F

Wind: 10 mph

Humidity: 63%

Total Precip: 0"

Attachments: 2



Jul 20, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:58

-Opened site: unlocked upper main and south side door, lower level door, job box, turned on power, and completed a perimeter sweep

-Assisting and supervising CWAM

-Assisting and supervising Summit Fire

-Owner Ben arrived at 1:30 and left at 1:45 for a viewing

Left at 1:47

Arrived back at 2:47

-Took out small trash cans and lightly organized site

-Replaced two studs in upper level due to warping

-Went over site progress with CWAM and Summit Fire

-Closed site: Locked all doors, job box, CWAMS pod (left unlocked), closed all windows, turned off all power, completed perimeter sweep

Left at 3:49

Weather Conditions:

Mostly sunny Mon, Jul 20, 2026, 8:58 AM



98°F

62°F

Wind: 10 mph

Humidity: 68%

Total Precip: 0"

Attachments: 0

Jul 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:
Arrived @ 2pm.
Weather Conditions:
Mostly sunny Mon, Jul 20, 2026, 2:18 PM

 Mostly sunny
92°F Wind: 12 mph
53°F Humidity: 95%
Total Precip: 0"

Attachments: 0

Jul 16, 2026

Job: 2927 W Pikes Peak Ave
Title: Summit Fire
Added By: Marlowe Downey
Log Notes:
Arrived at 8:53
-Set up tools and equipment in upper level
-Continuing to install and cut pipe for upper level runs
Weather Conditions:
Mostly sunny Thu, Jul 16, 2026, 9:04 AM

 **87°F** Wind: 15 mph
59°F Humidity: 67%
Total Precip: 0"

Attachments: 1




Jul 16, 2026

Job: 2927 W Pikes Peak Ave
Title: CWAM - HVAC
Added By: Marlowe Downey
Log Notes:
Arrived at 7:00
-Set up tools and equipment in upper level
-Continuing work on ducting runs and 90 degrees in the sanctuary
Weather Conditions:
Mostly sunny Thu, Jul 16, 2026, 8:35 AM

 **87°F** Wind: 15 mph
59°F Humidity: 66%

Total Precip: 0"

Attachments: 3



Jul 16, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:50

-Opened site: unlocked upper main and south side door, lower level door, job box, turned on power, and completed a perimeter sweep

-Organized and swept up from yesterdays work conducted by the ownership team and CWAM

-Continuing site maintenance

-Assisting and supervising CWAM

-Assisting and supervising Summit Fire

-Consolidated tools from lower level to job box due to the ownership teams absence for the rest of the week

Closed site and left at 4:30

Weather Conditions:

Mostly sunny Thu, Jul 16, 2026, 8:20 AM



83°F

56°F

Wind: 13 mph

Humidity: 72%

Total Precip: 0"

Attachments: 1



Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp Excavation

Added By: Marlowe Downey

Log Notes:

Arrived at 9:54 with CSU

-Working on main water flow and connection

-Fire department was not called to site and did not show up

Weather Conditions:

Mostly sunny Wed, Jul 15, 2026, 9:56 AM



87°F

57°F

Wind: 17 mph

Humidity: 71%

Total Precip: 0"

Attachments: 5



Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site: unlocked upper main and south side door, lower level door, job box, turned on power, and completed a perimeter sweep

-Organized and swept up from yesterdays work conducted by the ownership team and CWAM

-Walked grounds and picked up trash

-Assisting and supervising Summit Fire

-Assisting and supervising American Electrician

-Assisting and supervising owner ship team

-Delivered 6 - 2 3/4" tap cons for bottom plate of framing

Weather Conditions:

Sunny Wed, Jul 15, 2026, 8:17 AM



88°F

56°F

Wind: 18 mph

Humidity: 72%

Total Precip: 0"

Attachments: 1



Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 4:45pm.

Inspected, locked up, powered down, and closed the site @ 5pm.

Weather Conditions:

Mostly sunny Wed, Jul 15, 2026, 5:03 PM



Mostly sunny

86°F

56°F

Wind: 16 mph

Humidity: 72%

Total Precip: 0"

Attachments: 0

Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 8:30

-Set up tools and equipment in upper level

-Continuing and finishing all upper level ducting (covering the louvre, consolidate material from lower level to upper level, stub out ERV 3 and 4)

Left @ 4:45pm.

Weather Conditions:

Sunny Wed, Jul 15, 2026, 8:47 AM



88°F

56°F

Wind: 18 mph

Humidity: 72%

Total Precip: 0"

Attachments: 1



Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: American Electrician

Added By: Marlowe Downey

Log Notes:

Arrived at 8:15

-Began setting up tools and material at the exterior box

-Continuing box and line installation

Left @ 4:45pm

Weather Conditions:

Sunny Wed, Jul 15, 2026, 8:17 AM



88°F

56°F

Wind: 18 mph

Humidity: 72%

Total Precip: 0"

Attachments: 4



Jul 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:00

-Set up tools and equipment in upper level sanctuary

-Began taking in pipe for later threading and installment

Left @ 4pm.

Weather Conditions:

Sunny Wed, Jul 15, 2026, 8:17 AM



88°F

Wind: 18 mph

56°F

Humidity: 72%

Total Precip: 0"

Attachments: 1



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 9:30

-Set up tools and equipment in upper level

-Cutting and threading pipe from pipe delivery for upper level installations

Weather Conditions:

Sunny Tue, Jul 14, 2026, 10:50 AM



84°F

Wind: 17 mph

53°F

Humidity: 73%

Total Precip: 0"

Attachments: 1



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: Whitcomb Plumbing

Added By: Marlowe Downey

Log Notes:

Arrived at 9:40

-Reviewed site objectives with Caleb (scan site for any incomplete stub outs, any uninstalled line called out on plan, and complete overall plumbing work for drywall readiness)

-Set up tools and equipment in lower level for stub out completion

Weather Conditions:

Sunny Tue, Jul 14, 2026, 9:45 AM



85°F

53°F

Wind: 19 mph

Humidity: 86%

Total Precip: 0"

Attachments: 1



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: American Electrician

Added By: Marlowe Downey

Log Notes:

Arrived at 8:45

-Met with Caleb and went over site and objectives

-Worked on main exterior box and hook up to interior lines

Weather Conditions:

Sunny Tue, Jul 14, 2026, 9:01 AM



84°F

53°F

Wind: 17 mph

Humidity: 73%

Total Precip: 0"

Attachments: 3



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp Excavation

Added By: Marlowe Downey

Log Notes:

Arrived at 8:10

-Flushed the main line for future connection tomorrow with CSUs supervision

Left at 9:30

Weather Conditions:

Sunny Tue, Jul 14, 2026, 8:16 AM



87°F

55°F

Wind: 19 mph

Humidity: 72%

Total Precip: 0"

Attachments: 1



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:05

-Set up tools and equipment in upper level

-Completed ERVs (ran exhaust outputs closer than 10ft away recommended room distance however in the case of ducting being in the attic: recommendation is void, more 90 degree ducting was required than original plan however will not affect performance drastically)

-Will be adjusting placement of furnace threes ducting

-Organized and cleaned space

Weather Conditions:

Sunny Tue, Jul 14, 2026, 7:00 AM



87°F

59°F

Wind: 18 mph

Humidity: 71%

Total Precip: 0"

Attachments: 4



Jul 14, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:51

-Opened site: unlocked upper level main and south side door, unlocked lower level door, job box, turned on power, completed perimeter sweep

-Continued site maintenance

-Organized and cleaned lower level in preparation for owners arrival and work load

-Assisted and supervised CWAM

-Assisted and supervised ownership team

-Supervised Summit Fire

Left at 12:30 for schedule organization

Arrived back at 1:00

-Dismantled very first fence section to the right coming out of south side upper level door for electricians access to install hardware

-Reviewed completed work with CWAM and gathered any necessary information

Left at 1:45

Weather Conditions:

Sunny Tue, Jul 14, 2026, 7:00 AM



87°F

Wind: 18 mph

59°F

Humidity: 71%

Total Precip: 0"

Attachments: 0

Jul 13, 2026

Job: 2927 W Pikes Peak Ave

Title: American electrician + csu

Added By: Caleb Strickler

Log Notes:

Onsite to review new service feed. American electric will get new weather mast, panels, CT and disconnects set up for csu to run new service line while leaving existing service in place. Once new service is ran we can set up switchover with minimal power interruptions.

Weather Conditions:

Sunny Mon, Jul 13, 2026, 1:29 PM



90°F

Wind: 15 mph

58°F

Humidity: 77%

Total Precip: 0"

Attachments: 3



Jul 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:45

- Set up tools and equipment in upper level
- Buttoning up piping in lower level and moving on to upper level
- Received delivery of additional parts

Weather Conditions:

Sunny Mon, Jul 13, 2026, 8:59 AM



90°F

58°F

Wind: 15 mph

Humidity: 83%

Total Precip: 0"

Attachments: 2



Jul 13, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

- Continuing to work on final furnace three registers and stub outs as well as the application of duct sealant
- Reviewed plans and work objective for the day
- Had partial inspection for the F3 unit. Signed off and ready to insulate installed ductwork

Left at 4:00

Weather Conditions:

Sunny Mon, Jul 13, 2026, 7:14 AM



90°F

58°F

Wind: 15 mph

Humidity: 83%

Total Precip: 0"

Attachments: 3



Jul 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:45

-Opened site: unlocked upper level main and south side door, unlocked lower level door, job box, turned on power, completed perimeter sweep

-Continuing site maintenance

-Assisting and supervising CWAM

Left at 9:03

Weather Conditions:

Sunny Mon, Jul 13, 2026, 7:14 AM



90°F

58°F

Wind: 15 mph

Humidity: 83%

Total Precip: 0"

Attachments: 1



Jul 10, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:40

-Continued vertical runs in the lower level to finish out and pipe for upper level

Left at 4:00

Weather Conditions:

Partly cloudy with isolated storms Fri, Jul 10, 2026, 8:36 AM



84°F

53°F

Wind: 8 mph

Humidity: 80%

Total Precip: 0.02"

Attachments: 0

Jul 10, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

-Continued to work on final furnace threes registers and stub outs (application of duct sealant)

Left at 3:00

Weather Conditions:

Partly cloudy with isolated storms Fri, Jul 10, 2026, 8:06 AM



81°F

54°F

Wind: 7 mph

Humidity: 70%

Total Precip: 0.02"

Attachments: 0

Jul 10, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site: unlocked upper main and south door, unlocked lower level door, job box, opened windows, turned on power, completed perimeter sweep

-Assisted and supervised CWAM

-Cleaned up grounds

-Went over the days objectives with Summit as well as CWAM

-Swept up after the trades

Left at around 10:30

Weather Conditions:

Partly cloudy with isolated storms Fri, Jul 10, 2026, 7:54 AM



84°F

56°F

Wind: 8 mph

Humidity: 76%

Total Precip: 0.06"

Attachments: 0

Jul 9, 2026

Job: 2927 W Pikes Peak Ave

Title: Owner Ship Team

Added By: Marlowe Downey

Log Notes:

Arrived at 10:00

-Built chases in lower level bathrooms

-Studded out kitchen closet

Left at 6:00

Weather Conditions:

Partly cloudy with showers and scattered storms Thu, Jul 9, 2026, 12:00 AM



83°F

60°F

Wind: 18 mph

Humidity: 69%

Total Precip: 0.14"

Attachments: 5



Jul 9, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 11:00

-Completed runs in lower level

-Started pipe assembly for upper level runs

Left at 4:15

Weather Conditions:

Partly cloudy with showers and scattered storms Thu, Jul 9, 2026, 12:00 AM



83°F

60°F

Wind: 18 mph

Humidity: 69%

Total Precip: 0.09"

Attachments: 0

Jul 9, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

-Set up tools and equipment in upper level

-Began planning for duct work in sanctuary

-Continued applying duct sealant to attic ducting

-Assisted StreamHome with horizontal member installation in sanctuary

-Brought up needed ducting into attic of sanctuary for tomorrows construction

Left at 3:35

Weather Conditions:

Partly cloudy with showers Thu, Jul 9, 2026, 7:34 AM



83°F

58°F

Wind: 9 mph

Humidity: 68%

Total Precip: 0.1"

Attachments: 2



Jul 9, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:52

-Opened site: Unlocked upper level main and south doors, lower level door, job box, turned on power, opened windows, and completed perimeter sweep

-Organized and cleaned up from yesterdays work

-Organized with CWAM team on todays objective and job details

Left at 7:37

Arrived back at 9:18

-Delivered scrap and full piece lumber from other site

-Assisted and supervised owner ship team

-Assisted and supervised CWAM

-Re installed horizontal joists in sanctuary with CWAMS assist

-Completely swept building

-Went over site plan with CWAM

-Organized tools back

-Owner was still working after departure

Left at 4:20

Weather Conditions:

Partly cloudy with showers Thu, Jul 9, 2026, 7:34 AM



83°F

58°F

Wind: 9 mph

Humidity: 68%

Total Precip: 0.1"

Attachments: 2



Jul 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 7:45

- Set up tools and equipment in lower level
- Continued vertical sprinkler head installation as well as main pipe run down the main hallway in lower level
- Discussed site details and plans regarding attic sprinkler coverage with Caleb

Left at 3:30

Weather Conditions:

Partly cloudy with chance of storms Wed, Jul 8, 2026, 8:33 AM



81°F

58°F

Wind: 24 mph

Humidity: 61%

Total Precip: 0.06"

Attachments: 1



Jul 8, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 8:35

- Continued attic duct runs as well as applying duct sealant in rooms 203 and 202
- Will soon wrap up ducting work in the sanctuary
- Poured concrete in lower level utility/storage room
- Cleaned up and organized material in attic

Left at 4:00

Weather Conditions:

Partly cloudy with chance of storms Wed, Jul 8, 2026, 8:33 AM



81°F

58°F

Wind: 24 mph

Humidity: 61%

Total Precip: 0.06"

Attachments: 2



Jul 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:51

- Opened site: unlocked upper level main and south doors, unlocked lower level door, turned on power, completed perimeter sweep
- Organized tools and equipment used by the owner ship team in lower level and job box
- Delivered circular saw for later owner ship team use
- Swept up all areas worked in yesterday as well as stairwells
- Organized ducting in upper level rooms
- Currently continuing site maintenance
- Supervising Summit Fire
- Assisting and supervising CWAM
- Delivered screw jack base plate for scaffold
- Blocked off storage room after concrete was poured for drain
- Disassembled scaffold
- Cleaned and organized up after trades

Left at 2:50 for other site

Arrived back at 4:00

- Closed site

Left at 4:30

Weather Conditions:

Partly cloudy with showers Wed, Jul 8, 2026, 7:02 AM



88°F

58°F

Wind: 10 mph

Humidity: 74%

Total Precip: 0.03"

Attachments: 4



Jul 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Ownership Team

Added By: Marlowe Downey

Log Notes:

Arrived at 9:00

- Set up equipment and tools in lower level
- Continuing chase work in lower level (rooms: 104 and 101)
- Scheduled to start playground work at 11:00 with Caleb

Weather Conditions:

Partly cloudy with isolated storms Tue, Jul 7, 2026, 9:06 AM



92°F

57°F

Wind: 11 mph

Humidity: 73%

Total Precip: 0.01"

Attachments: 2



Jul 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:10

-Set up tools and equipment in lower level

-Continuing vertical stub outs from the main lines in lower level

Weather Conditions:

Partly cloudy with isolated storms Tue, Jul 7, 2026, 8:00 AM



92°F

Wind: 11 mph

57°F

Humidity: 73%

Total Precip: 0"

Attachments: 0

Jul 7, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:10

-Set up tools and equipment in upper level

-Began sealing and routing duct in the attic

-Was notified by Caleb bathroom fan ducting in lower level 109, must be manipulated for proper chase construction. Manny gave approval of manipulation and says cfm inspection will pass

-Built and ran ducting from fresh air intake system to classroom 203

-Cleaned up and organized work area

Left at 4:00

Weather Conditions:

Partly cloudy with isolated storms Tue, Jul 7, 2026, 7:00 AM



92°F

Wind: 11 mph

57°F

Humidity: 73%

Total Precip: 0"

Attachments: 5



Jul 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site: unlocked upper level main door and south side door, lower level door, job box, turned on power, opened windows, completed perimeter sweep

-Continued site maintenance

-Assisted and supervised CWAM

-Logged all needed areas for nail plates to Caleb

-Supervised Summit Fire

-Supervised and assisted owners

Left at 12:44

Weather Conditions:

Partly cloudy with isolated storms Tue, Jul 7, 2026, 7:00 AM



92°F

Wind: 11 mph

57°F

Humidity: 73%

Total Precip: 0"

Attachments: 0

Jul 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Caleb Strickler

Log Notes:

Continued basement pipe work.

Weather Conditions:

Partly cloudy with patchy smoke Mon, Jul 6, 2026, 3:28 PM



88°F

Wind: 8 mph

60°F

Humidity: 50%

Total Precip: 0"

Attachments: 0

Jul 6, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM

Added By: Caleb Strickler

Log Notes:

Continued attic equipment setting and connections. Got confirmation efflorescence sump pump is getting concrete on Wednesday.

Weather Conditions:

Partly cloudy with patchy smoke Mon, Jul 6, 2026, 3:28 PM



88°F

60°F

Wind: 8 mph

Humidity: 50%

Total Precip: 0"

Attachments: 0

Jul 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:30

-Set up tools and equipment in lower level

-Continued vertical sprinkler runs

-Reviewed crucial sprinkler runs with Caleb (stair way connecting the lower level to upper level must be framed for needed run)

Weather Conditions:

Partly cloudy with patchy smoke Mon, Jul 6, 2026, 9:14 AM



87°F

58°F

Wind: 12 mph

Humidity: 87%

Total Precip: 0"

Attachments: 0

Jul 6, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:45

-Set up tools and equipment in upper level

-Finished vent installment and built nesenary ducting

-Scheduled to start installing ERVs soon

Weather Conditions:

Partly cloudy with patchy smoke Mon, Jul 6, 2026, 9:59 AM



92°F

60°F

Wind: 10 mph

Humidity: 56%

Total Precip: 0"

Attachments: 4



Jul 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:54

-Opened site: Unlocked upper level main and south door, unlocked lower level door, unlocked job box, turned on power, completed perimeter sweep

-Rolled up and stowed away American Electrician sign

-Organized and cleaned up from last thursdays work

-Picked up trash from property grounds and organized material in between conex

-Currently continuing site maintenance

-Assisting and supervising CWAM

-Assisting and supervising Owners

-Supervising Summit Fire

-Disposed of trash from large garbage cart in dumpster

-Adjusted gate door for proper swing

Left at 11:09

Weather Conditions:

Partly cloudy with patchy smoke Mon, Jul 6, 2026, 7:13 AM



90°F

57°F

Wind: 11 mph

Humidity: 51%

Total Precip: 0"

Attachments: 0

Jul 2, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Caleb Strickler

Log Notes:

Worked on basement fire line connections

Weather Conditions:

Sunny with patchy smoke Thu, Jul 2, 2026, 10:08 AM



90°F

59°F

Wind: 13 mph

Humidity: 59%

Total Precip: 0"

Attachments: 1



Jul 2, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM

Added By: Caleb Strickler

Log Notes:

Weather Conditions:

Sunny with patchy smoke Thu, Jul 2, 2026, 10:08 AM



90°F

59°F

Wind: 13 mph

Humidity: 59%

Total Precip: 0"

Attachments: 10



Jul 1, 2026

Job: 2927 W Pikes Peak Ave

Title: Owner team

Added By: Caleb Strickler

Log Notes:

Worked on installing basement steel supports

Weather Conditions:

Sunny Wed, Jul 1, 2026, 12:00 AM



91°F

54°F

Wind: 10 mph

Humidity: 52%

Total Precip: 0"

Attachments: 10



Jul 1, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM

Added By: Caleb Strickler

Log Notes:

Continued working on attic mechanical and fresh air intake louver

Weather Conditions:

Sunny Wed, Jul 1, 2026, 12:00 AM



91°F

54°F

Wind: 10 mph

Humidity: 52%

Total Precip: 0"

Attachments: 0

Jul 1, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 9:00

-Set up equipment and tools in upper level

-Continuing to frame attic window as well as applying duct sealant

Weather Conditions:

Partly cloudy with patchy smoke Wed, Jul 1, 2026, 9:02 AM



88°F

60°F

Wind: 17 mph

Humidity: 53%

Total Precip: 0"

Attachments: 4



Jul 1, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:25

- Informed yesterday's absence was due to a parts run in Denver
- Set up equipment and tools in lower level
- Unloaded parts from yesterday's inventory run
- Continuing sprinkler vertical runs

Weather Conditions:

Partly cloudy with patchy smoke Wed, Jul 1, 2026, 9:02 AM



88°F

60°F

Wind: 17 mph

Humidity: 53%

Total Precip: 0"

Attachments: 0

Jul 1, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

- Opened site: unlocked main and south side upper level doors, unlocked lower level door, unlocked job box, opened windows in upper level, turned on power, completed perimeter sweep
- Continued site maintenance: organization of material from owners labor yesterday and today, swept up debris from yesterday's work and today
- Assisted and supervised CWAM with framing the attic vent
- Assisted and supervised owners with precision drilling for L beam installation

Left at 12:20

Weather Conditions:

Partly cloudy with patchy smoke Wed, Jul 1, 2026, 7:31 AM



85°F

60°F

Wind: 18 mph

Humidity: 50%

Total Precip: 0"

Attachments: 7



Jun 30, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM

Added By: Caleb Strickler

Log Notes:

Continued setting attic duct and equipment, applied duct sealant to attic ducting, assisted Marlowe with attic window removal, framed attic window cut out for new vent installation, cleaned up attic, left at 4:20

Weather Conditions:

Partly cloudy with patchy smoke Tue, Jun 30, 2026, 9:15 AM



82°F

50°F

Wind: 22 mph

Humidity: 69%

Total Precip: 0"

Attachments: 3



Jun 30, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site: unlocked main and south side upper level doors, unlocked lower level doors, opened upper level windows, turned on all power

-Continuing site maintenance: sweeping, organizing, and trash removal around property

-Notched out blocking for sprinkler system piping

-Readied hammer drill and equipment needed for L bracket installment

Left at 8:05 for maintenance call after Caleb arrived

Arrived back at 9:30

-Delivered 27 ft ladder for future window removal

Left at 9:35

Arrived back at 11:15

-Took out attic window with CWAM techs

-Cleaned debris from demo of window

-Assisted owners with L bracket holes

-Cleaned up area the trades and owners worked in

-Closed site: Locked all doors and windows, locked job box, took 27ft ladder inside, turned off power, completed final perimeter sweep

Left at 4:35

Weather Conditions:

Partly cloudy with patchy smoke Tue, Jun 30, 2026, 7:16 AM



81°F

50°F

Wind: 22 mph

Humidity: 78%

Total Precip: 0"

Attachments: 3



Jun 30, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels

Added By: Stephen Michaels

Log Notes:

Arrived @ 3pm.

Supervised site while Marlowe picked up osb for the exterior vent.

Spoke with Caleb and Lee concerning tomorrow's scope of work.

Left @ 4pm.

Weather Conditions:

Partly cloudy with patchy smoke Tue, Jun 30, 2026, 3:02 PM



Partly cloudy with patchy smoke

86°F

56°F

Wind: 19 mph

Humidity: 65%

Total Precip: 0"

Attachments: 0

Jun 29, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Caleb Strickler

Log Notes:

Finished up what he could in the basement for now. Worked on penetrations and preparations for the upper level

Weather Conditions:

Sunny Mon, Jun 29, 2026, 12:00 AM



91°F
61°F

Wind: 14 mph
Humidity: 43%
Total Precip: 0"

Attachments: 4



Jun 29, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:05

- Set up tools and equipment for today's work objectives
- Began reviewing plan sheet and continuing to apply duct sealant
- Completed 3 new duct runs and drops in the attic

Left at 4:00

Weather Conditions:

Sunny with patchy smoke Mon, Jun 29, 2026, 7:28 AM



89°F
68°F

Wind: 16 mph
Humidity: 19%
Total Precip: 0"

Attachments: 2



Jun 29, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

- Opened site: unlocked main and south side upper level doors, unlocked lower level door, unlocked job box, turned on all power, opened upper level windows
- Cleaned up trash from homeless in the lower level stair well
- Continued to maintain the site

-Met with Caleb at 7:30, Caleb discussed site plans and issues with CWAM

Left at 8:50

Weather Conditions:

Sunny with patchy smoke Mon, Jun 29, 2026, 7:28 AM



89°F

68°F

Wind: 16 mph

Humidity: 19%

Total Precip: 0"

Attachments: 1



Jun 29, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 8:45

-Set up equipment and tools in the lower level

-Installed more laterals in lower level (will be fully completed tomorrow)

-Cleaned up area and organized tools into the kitchen

Left at 4:00

Weather Conditions:

Sunny Mon, Jun 29, 2026, 12:00 AM



91°F

61°F

Wind: 14 mph

Humidity: 43%

Total Precip: 0"

Attachments: 0

Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: PPRBD - Duct inspection

Added By: Marlowe Downey

Log Notes:

Arrived at 1:50

-Inspected partial pass : upper level ABOVE CEILING DUCT - SUPPLY/RETURN MAINS/BRANCHES FOR F-1 & F-2 OK TO WRAP. EXHAUST DUCT FOR EF-1, 2, 3 & 4 COMPLETE. splice still needs to be uploaded when we receive it

Left at 2:12

Weather Conditions:

Partly cloudy with showers Fri, Jun 26, 2026, 2:07 PM



78°F

54°F

Wind: 14 mph

Humidity: 98%

Total Precip: 0.07"

Attachments: 1



Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: CS Quality Roofing

Added By: Casey Copley

Log Notes:

Arrived at 12 pm, set up ladder to steeple, repaired shingle, looked at radon penetrations on main roof, got a materials list together to dry those in, he will be back on Monday to install the 2 roof boots,

Weather Conditions:

Partly cloudy with chance of storms Fri, Jun 26, 2026, 1:06 PM



83°F

Wind: 8 mph

57°F

Humidity: 91%

Total Precip: 0.04"

Attachments: 0

Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 7:15

-Began work in lower level tying all lines together

-Started work in upper level and insured all runs from lower level will tie in correctly

Left at 1:00

Weather Conditions:

Partly cloudy with showers Fri, Jun 26, 2026, 7:50 AM



82°F

Wind: 9 mph

54°F

Humidity: 96%

Total Precip: 0.07"

Attachments: 0

Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 6:00

-Opened site: turned on lights and opened lower level door

-Began running more duct in the attic

Weather Conditions:

Partly cloudy with showers Fri, Jun 26, 2026, 7:50 AM



82°F

54°F

Wind: 9 mph

Humidity: 96%

Total Precip: 0.07"

Attachments: 1



Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-CWAM had already opened site

-Opened site fully: unlocked job box and main upper level door, turned on fans, completed perimeter sweep

-Assisted and supervised CWAM

-Assisted and supervised Summit Fire

-Consolidated material from yesterday's work

Left at 8:12

Arrived back at 1:00

-Sweeping up and attending to all trades on site

Weather Conditions:

Partly cloudy with showers Fri, Jun 26, 2026, 7:45 AM



82°F

54°F

Wind: 8 mph

Humidity: 96%

Total Precip: 0.06"

Attachments: 0

Jun 26, 2026

Job: 2927 W Pikes Peak Ave

Title: American Electrician

Added By: Marlowe Downey

Log Notes:

Arrived at 10:00

-Set up work area in the south side yard

-Currently installing electrical power box south side of building in between the sanctuary windows and exterior entrance

Cleaned up and left @ 6pm.

Weather Conditions:

Partly cloudy with chance of storms Fri, Jun 26, 2026, 1:06 PM

**83°F****57°F**

Wind: 8 mph

Humidity: 91%

Total Precip: 0.04"

Attachments: 3



Jun 25, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 7:33

-Set up in lower level

-Continued run work in lower level

-Had to leave early due to drilling issue on exterior wall

Left at 2:45

Weather Conditions:

Partly cloudy with isolated storms Thu, Jun 25, 2026, 7:35 AM

**78°F****58°F**

Wind: 9 mph

Humidity: 80%

Total Precip: 0.13"

Attachments: 0

Jun 25, 2026

Job: 2927 W Pikes Peak Ave

Title: Whitcomb Plumbing

Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

-Began work in lower level

-Installing exterior water spigot

Weather Conditions:

Partly cloudy with nearby thunderstorms Thu, Jun 25, 2026, 7:19 AM

**71°F****56°F**

Wind: 10 mph

Humidity: 91%

Total Precip: 0.12"

Attachments: 0

Jun 25, 2026

Job: 2927 W Pikes Peak Ave
Title: CWAM - HVAC
Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

-Set up equipment for today's work objectives

-Continued to apply duct sealant in attic as well as constructing more duct runs

Left at 4:15

Weather Conditions:

Partly cloudy with nearby thunderstorms Thu, Jun 25, 2026, 7:19 AM



71°F

56°F

Wind: 10 mph

Humidity: 91%

Total Precip: 0.12"

Attachments: 1



Jun 25, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 6:56

-Opened site: unlocked south and main upper level doors, unlocked lower level door and job box, turned on all power, performed perimeter sweep

-Continued site maintenance

-Assisted and supervising CWAM

-Assisted and supervising Whitcomb plumbing

-Assisted and supervising Summit Fire

Left at 8:20

Weather Conditions:

Partly cloudy with nearby thunderstorms Thu, Jun 25, 2026, 7:19 AM



71°F

56°F

Wind: 10 mph

Humidity: 91%

Total Precip: 0.12"

Attachments: 0

Jun 25, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Marlowe opened site, I arrived at 8 am, set up, supervision, scheduling, left site at 9:40 for leadership meeting at the office, arrived back on site at 1pm, worked on vacation plan and look ahead, site cleaning, ownership team worked on infilling subfloor, secured and closed site at 4:20 pm

Weather Conditions:

Partly cloudy with isolated storms Thu, Jun 25, 2026, 6:35 AM



Partly cloudy with isolated storms

78°F**59°F**

Wind: 20 mph

Humidity: 89%

Total Precip: 0.13"



Job: 2927 W Pikes Peak Ave
Title: Nelson And Ross site meeting
Added By: Marlowe Downey

Log Notes:

Arrived at 12:40

-Very shortly discussed architectural problem with Manny, told many the issue wasn't in his realm and he needed to call Brian
Left at 12:45

- Casey and Caleb spoke with the architect and requested a framing solution to the issue instead of another ducting revision
-Awaiting confirmation from architect and engineer

Weather Conditions:

Partly cloudy with thunderstorms Wed, Jun 24, 2026, 1:02 PM



80°F

58°F

Wind: 17 mph

Humidity: 96%

Total Precip: 0.09"

Attachments: 1



Jun 24, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Services - HVAC
Added By: Marlowe Downey

Log Notes:

Arrived at 8:45

-Prepared for work objectives

-Continuing to apply duct sealant to attic ducting

-Continuing duct modification for optimal fitment

-Installed sump pump in lower level

-Manny discussed architectural contradiction and mechanical issues with Lole the Architect briefly (Lole informed issues were out of his scope and Brian will be contacted)

-Shane cleaned up area and left at 1:05

-Manny and Roy met with PPRBD duct insulation inspection (only ERV is required for inspection)

-Cleaned floor space under work environment and attic

Left at 3:40

Weather Conditions:

Partly cloudy with thunderstorms Wed, Jun 24, 2026, 9:01 AM



81°F

58°F

Wind: 17 mph

Humidity: 99%

Total Precip: 0.05"

Attachments: 9



Jun 24, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived 6:53

-Opened site: Unlocked south, main entry, and lower level doors, unlocked job box, opened windows, turned on power, preformed perimeter sweep

-Re-hung bank banner

-During a tidy of the property grounds noticed all the fencing in between the pods was stolen

-Supervised and assisted CWAM

-Supervised and assisted Summit Fire

-Assisted Sean and John with equipment and material needs as they worked on sub flooring, chases, and planning for playground

-Cleaned up after all trades

-Organized and maintained site

-Closed site: locked all doors, windows, job box, turned off power

Left at 3:54

Weather Conditions:

Partly cloudy with thunderstorms Wed, Jun 24, 2026, 7:01 AM



80°F

58°F

Wind: 14 mph

Humidity: 83%

Total Precip: 0"

Attachments: 3



Jun 24, 2026

Job: 2927 W Pikes Peak Ave
Title: PPRBD - Ducting Insulation Inspection
Added By: Marlowe Downey

Log Notes:

Arrived at 2:10

-Splice is required to be uploaded to PPRBD website for finalization,

-Only ERV insulation requires inspection

Left at 2:20

Weather Conditions:

Partly cloudy with nearby thunderstorms Wed, Jun 24, 2026, 2:17 PM



79°F

56°F

Wind: 16 mph

Humidity: 89%

Total Precip: 0.04"

Attachments: 2



Jun 24, 2026

Job: 2927 W Pikes Peak Ave
Title: Summit Fire
Added By: Marlowe Downey

Log Notes:

Arrived at 7:30

-Began preparing for work and setting up equipment in lower level

-Tech one is laying pipe in lower level and tech two is drilling holes for runs in upper level

-Lower level runs are scheduled for completion tomorrow

Left at 3:40

Weather Conditions:

Partly cloudy with thunderstorms Wed, Jun 24, 2026, 7:46 AM




80°F

58°F

Wind: 17 mph

Humidity: 90%

Total Precip: 0.16"

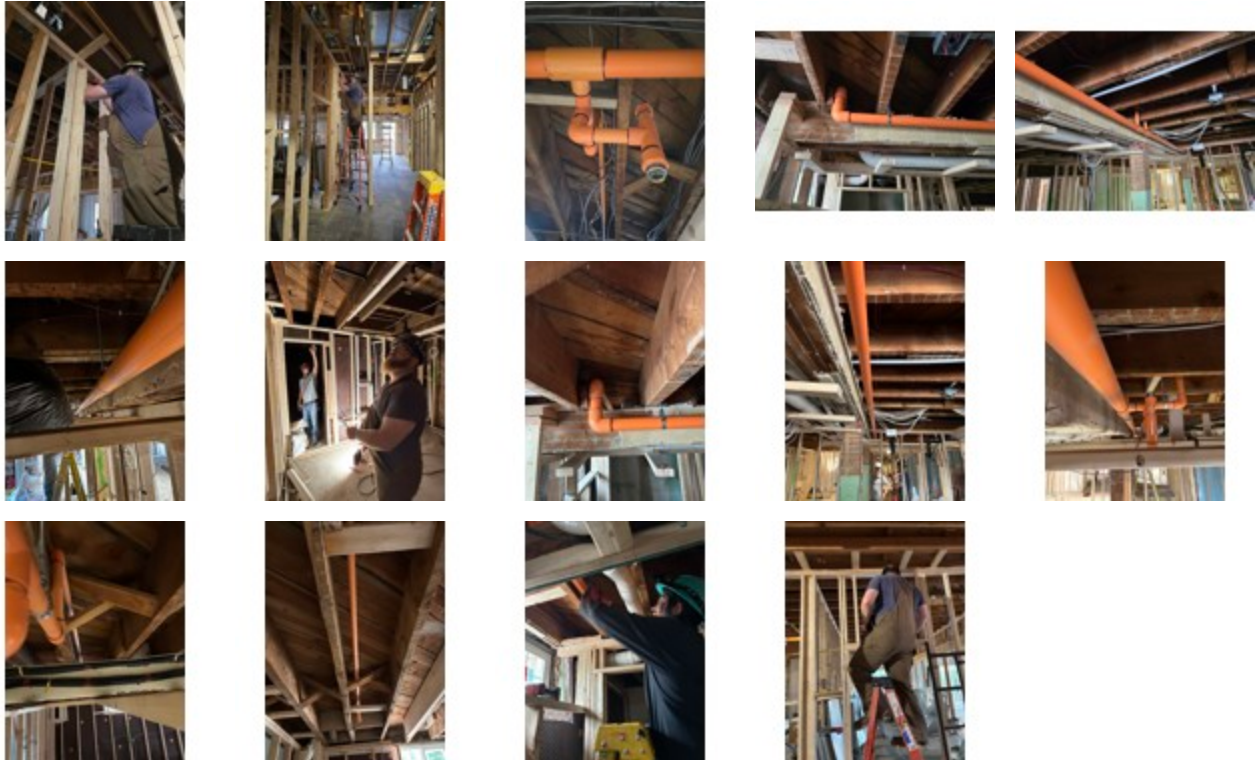

Jun 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:56

- Opened site: unlocked main and south upper level doors and lower level, turned on all equipment and lights, job box, and completed perimeter sweep
 - Swept upper level from yesterday
 - Supervising CWAM
 - Assisted CWAM in material relocation
 - Walked site with the owners, Casey, and Caleb (came to a decision on flooring and base cove)
 - Delivered 40 2x4x8
 - Supervised Summit Fire
 - Cleaned up after Summit Fire
 - Assisted John and Sean with equipment and material needs
 - Organized and swept up after all trades near end of day
 - Closed and locked site: Locked doors, windows, job box, turned off power
- Left at 4:45

Weather Conditions:

Partly cloudy with mist and fog Tue, Jun 23, 2026, 7:14 AM



88°F

60°F

Wind: 16 mph

Humidity: 98%

Total Precip: 0.01"



Jun 23, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Marlowe opened site, pm work in office with pm team, I arrived at 8 am, set up, on site oc / fire pipe meeting with Caleb and owners, supervision, scheduling, picked up additional framing lumber and delivered to site, site verifications and rfis, on site meeting with Caleb and CSU electrical division and they said that the electrical firm still needs to submit load calcs and other submittal docs for review and approval, caleb will address this issue ASAP, landscapers will be back next week to work on irrigation and plants, spoke with thorp excavation and requested the CSFD flush to be scheduled right away so we have the flush certificate for the suppression inspection whenneeded, he will schedule this and get back to me, had ownership team self perform chase framing in the lower level, site cleaning and organizing, received pods delivery, secured and closed site at 4:45.

Weather Conditions:

Partly cloudy with isolated storms Tue, Jun 23, 2026, 4:15 PM




Partly cloudy with isolated storms

84°F
59°F

Wind: 12 mph

Humidity: 100%

Total Precip: 0.06"

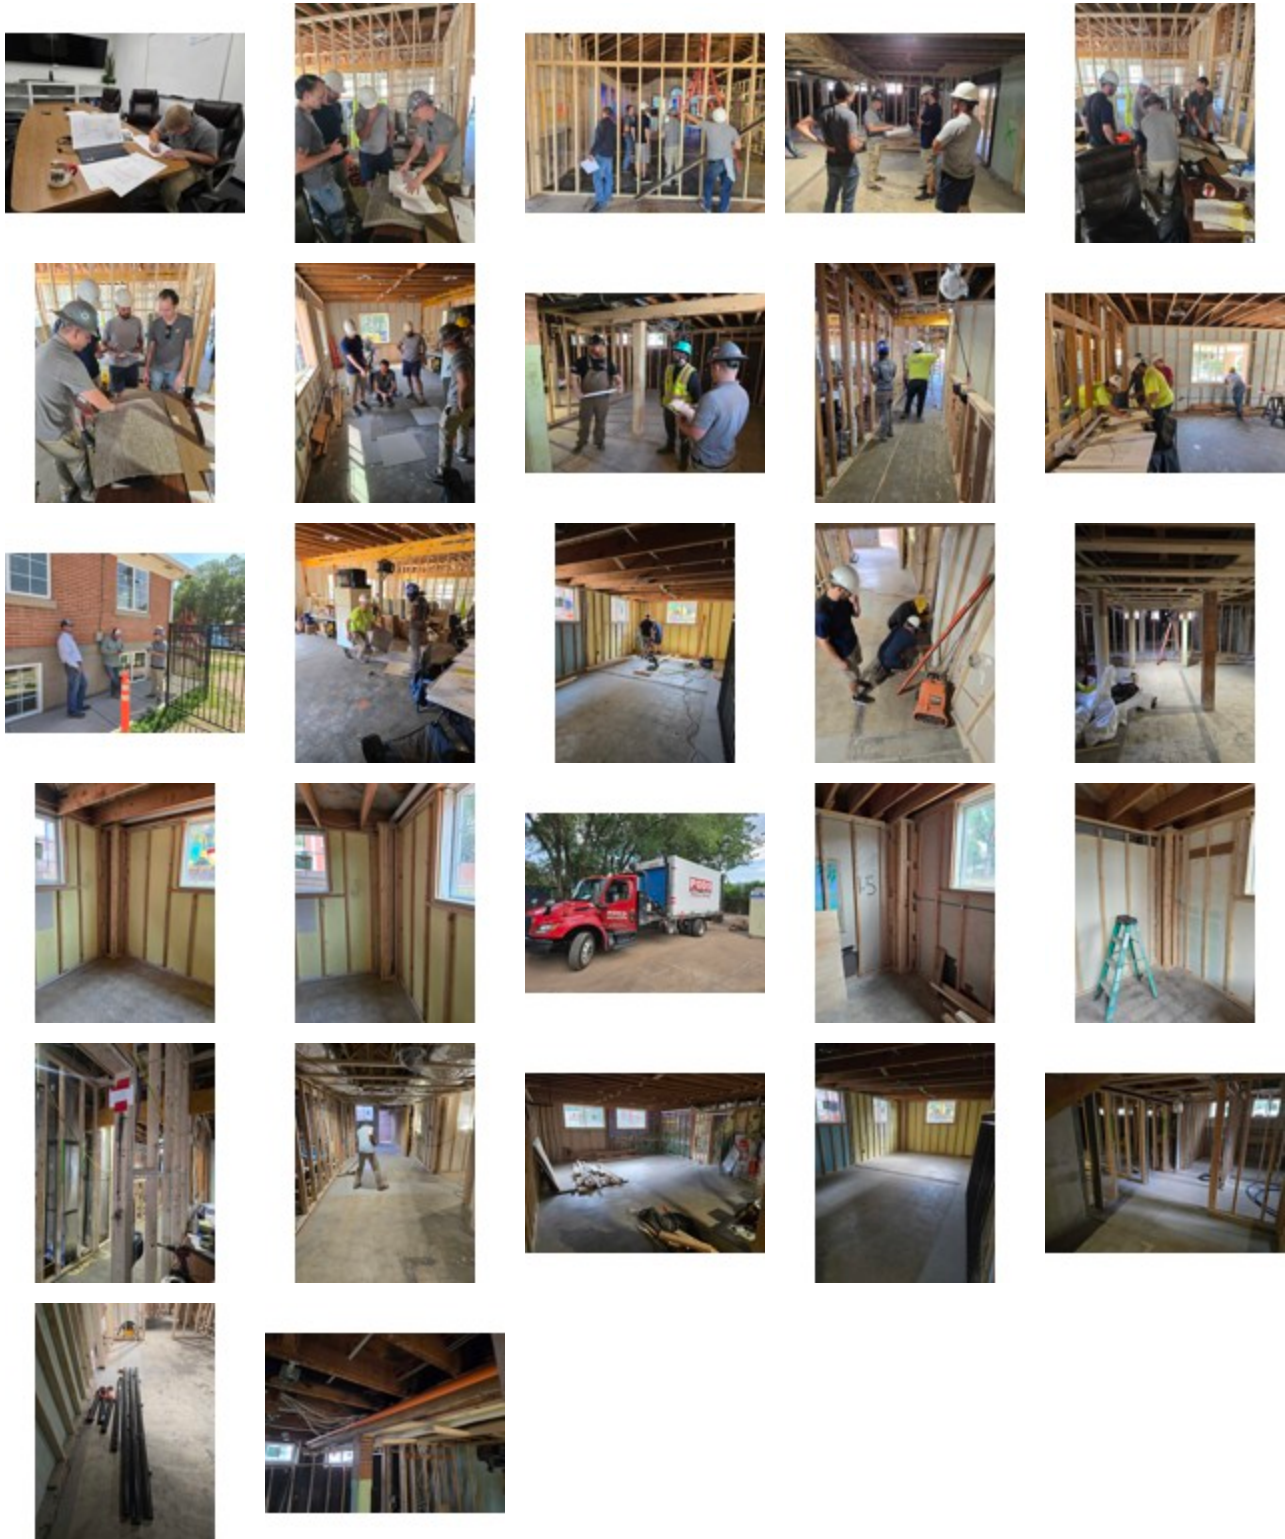

Jun 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Pods delivery

Added By: Casey Copley

Log Notes:

Pods delivered 2 units 1 at 10 am and 1 at 3 pm

Weather Conditions:

Partly cloudy with isolated storms Tue, Jun 23, 2026, 4:15 PM



Partly cloudy with isolated storms

84°F
59°F

Wind: 12 mph

Humidity: 100%

Total Precip: 0.06"

Attachments: 3



Jun 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Casey Copley

Log Notes:

Arrived at 10 am, unloaded cpvc materials and pipe, set up, demoed steel mains, began installing cpvc pipe, drilled out wall plates for routing, clean up left site at 4:30,

Weather Conditions:

Partly cloudy with isolated storms Tue, Jun 23, 2026, 4:15 PM



Partly cloudy with isolated storms

84°F
59°F

Wind: 12 mph

Humidity: 100%

Total Precip: 0.06"

Attachments: 15



Jun 23, 2026

Job: 2927 W Pikes Peak Ave
Title: G&K Landscaping
Added By: Marlowe Downey

Log Notes:

Arrived at 10:00
-Met with Casey
-Deep watered all plants
Scheduled to work on irrigation and landscaping next week

Weather Conditions:

Partly cloudy with showers Tue, Jun 23, 2026, 10:51 AM



83°F

57°F

Wind: 10 mph

Humidity: 93%

Total Precip: 0"

Attachments: 4



Jun 23, 2026

Job: 2927 W Pikes Peak Ave
Title: OC/Selection Meeting
Added By: Stephen Michaels

Log Notes:

Arrived @ 9am.
Shadowed OC/Selection meeting.
Helped Marlowe unload lumber.
Left @ 9:30am.

Weather Conditions:

Partly cloudy with showers Tue, Jun 23, 2026, 9:05 AM



Partly cloudy with showers

87°F

58°F

Wind: 10 mph

Humidity: 93%

Total Precip: 0.02"

Attachments: 3



Jun 23, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Services HVAC
Added By: Marlowe Downey

Log Notes:

Arrived at 7:00

- Set up equipment for today's work objectives
- Began vacuuming and cleaning out previously installed ductwork and making a material list
- Continued sealing ducting
- Reviewed plans and continued installing attic ductwork
- Completed all ducting installation in lower level
- Cleaned up and organized HVAC related materials

Left at 4:00

Weather Conditions:

Partly cloudy with mist and fog Tue, Jun 23, 2026, 7:30 AM



88°F

60°F

Wind: 15 mph

Humidity: 96%

Total Precip: 0"

Attachments: 5



Jun 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 6:56

- Opened site: unlocked main and back upper level doors as well as lower level, turned on all equipment and lights, performed perimeter sweep
- Supervised CWAM
- Swept upper level
- Swept up lower level
- Built chase in lower level classroom
- Framed door way and installed stud in bathroom in upper level
- Demoed side of soffit for summits ease of access in lower level classroom
- Cleaned up after CWAM
- Installed nailers and demoed stair way ceiling clearance and studded back out
- Met with Kelly and Sean (Kelly's father)
- Locked up site, windows, all doors, and job box, turned off lights and equipment

Left at 4:35

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 22, 2026, 7:28 AM

82°F

Wind: 18 mph

Humidity: 73%



55°F

Total Precip: 0.06"

Attachments:


4



Jun 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Marlowe opend site at 7am, I started the day at the office coordinating with the project management team, I arrived on site at 8 am, set up workstation, site inspection, supervision, scheduling, site verifications, spoke with Kelly on the phone and provided quick update, salvage demoed lower level soffit face in order to expand the soffit for the fire main, demoed lower level bulkhead on stairs to make head clearance, re framed bulkhead, site cleaning, worked on self performance task list and vacation plan while I am away, spoke with Whitcomb Plumbing and CSU needs additional paperwork and fees paid before they can schedule the meter swap, spoke with Caleb (pm) he will get with CSU and submit whatever we need and pay the associated fees so we can get CSU on our schedule adap, sent caleb photos of the back flow device and pupe sizing needed for the paperwork to submit, during close up of site met with Kelly and Sean and discussed site plans, left at 4:35

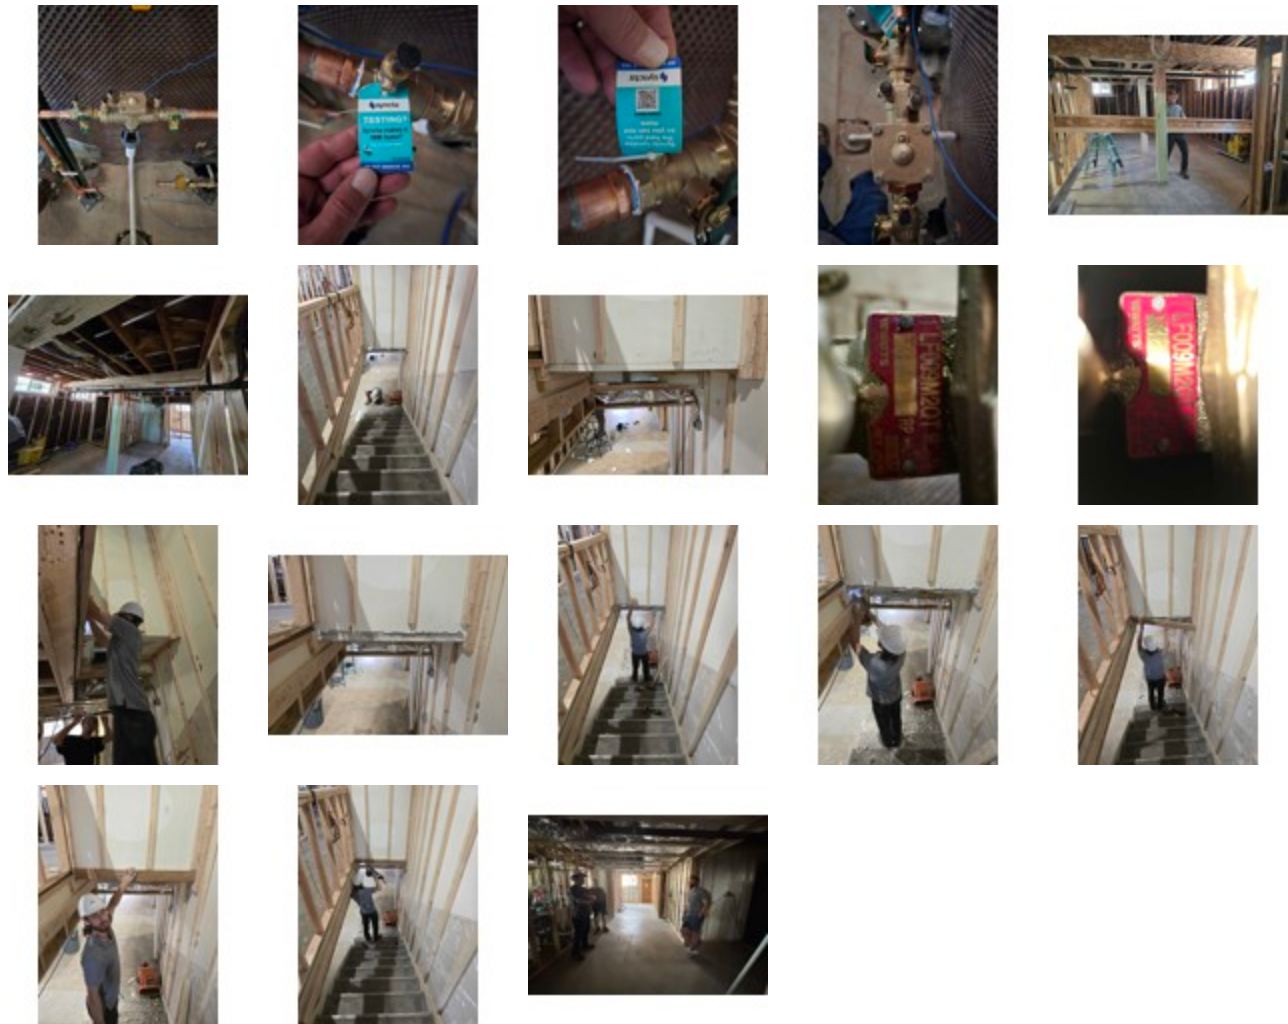

Jun 22, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Casey Copley

Log Notes:

Arrived at 10 am, unloaded and set up, began demo of previously installed sprinkler main, confirmed that they received revised plan from their engineers, packed up and left site to finalize the materials list so they can pick the materials up from Denver and get it on site asap,

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 22, 2026, 10:28 AM



Partly cloudy with isolated storms

84°F

53°F

Wind: 19 mph

Humidity: 77%

Total Precip: 0"

Attachments: 4



Jun 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC
Added By: Casey Copley

Log Notes:

Arrived at 9 am, set up, removed temporary heating air handlers and components, finished lower level ducting insulation, called for lower level insulation inspection for tomorrow, mixed mortar and applied mortar to exterior wall penetrations, applied fire foam to exterior penetration behind mortar, cleaned and left at 3:50

Attachments: 10



Jun 19, 2026

Job: 2927 W Pikes Peak Ave
Title: G&K Landscaping
Added By: Marlowe Downey

Log Notes:

Arrived at 9:20
-Deep watered all plants
Left at 10:08

Weather Conditions:

Partly cloudy with isolated storms Fri, Jun 19, 2026, 9:53 AM



83°F
50°F

Wind: 9 mph
Humidity: 68%
Total Precip: 0.03"

Attachments: 1



Jun 19, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 5:30

-Began work on shortening lower level hallway duct run for more space to install fire suppression system

-Continued runs in the attic

-Cleaned worked in areas and packed up

Left at 1:00

Weather Conditions:

Partly cloudy with isolated storms Fri, Jun 19, 2026, 8:08 AM



84°F

49°F

Wind: 10 mph

Humidity: 74%

Total Precip: 0.03"

Attachments: 3



Jun 19, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

-Met with CWAM and went over objectives for today

-Opened site completely

-Continuing to improve site quality

-Vacuumed unreachable channels in floor of upper level

-Began vacuuming lower level

-Reinstalled OSB on soffit in lower level kitchen area

-Assisted CWAM

-Cleaned up and locked entire site

Left at 1:05

Weather Conditions:

Partly cloudy with isolated storms Fri, Jun 19, 2026, 7:53 AM



81°F

50°F

Wind: 9 mph

Humidity: 76%

Total Precip: 0.01"

Attachments: 0

Jun 18, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 9:36

- Organized with Casey on the days objectives
- Worked on improving overall site conditions and space
- Swept entire parking lot
- Organized job box
- Organized Milwaukee pack outs
- Assisted CWAM
- Swept up after CWAM
- Trash pick up around property
- Ran all extension cords to walls and ceiling

Left at 4:48

Weather Conditions:

Mostly sunny Thu, Jun 18, 2026, 9:35 AM




84°F

56°F

Wind: 16 mph

Humidity: 51%

Total Precip: 0"

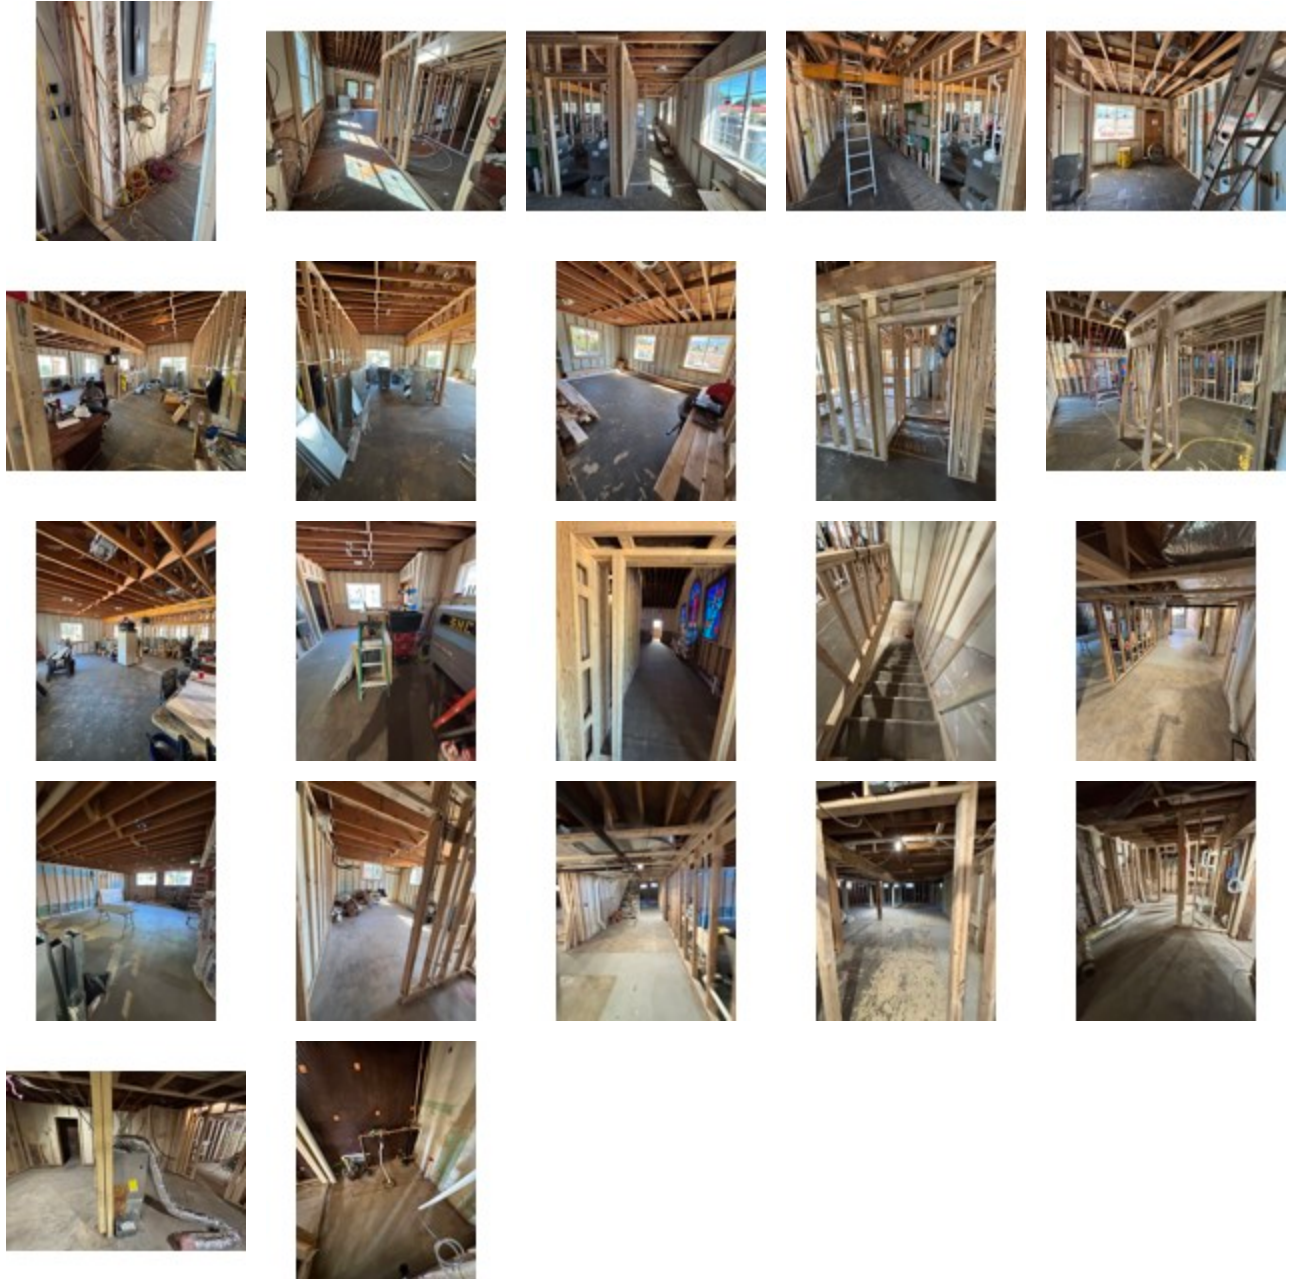

Jun 18, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Casey Copley

Log Notes:

Arrived at 2 pm, brought delivery inside, left at 3:30 pm

Weather Conditions:

Partly cloudy Thu, Jun 18, 2026, 4:19 PM

 Partly cloudy
80°F Wind: 26 mph
57°F Humidity: 48%
Total Precip: 0"

Attachments: 2



Jun 18, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Opened site, site inspection, set up workstation, cleaning, supervision, scheduling, pm work, met with Caleb and Lee on project coordination and plan forward with summit fire, received summit fire material delivery, began drafting letters of intent to subcontractors that are behind schedule, site verifications with subcontractors, called landscapers to request daily watering by hand with a water tank until we get the irrigation system installed, site cleaning and organization and material consolidation, secured and closed site at 5pm

Weather Conditions:

Partly cloudy Thu, Jun 18, 2026, 4:06 PM



Partly cloudy


76°F

51°F

Wind: 21 mph

Humidity: 55%

Total Precip: 0"

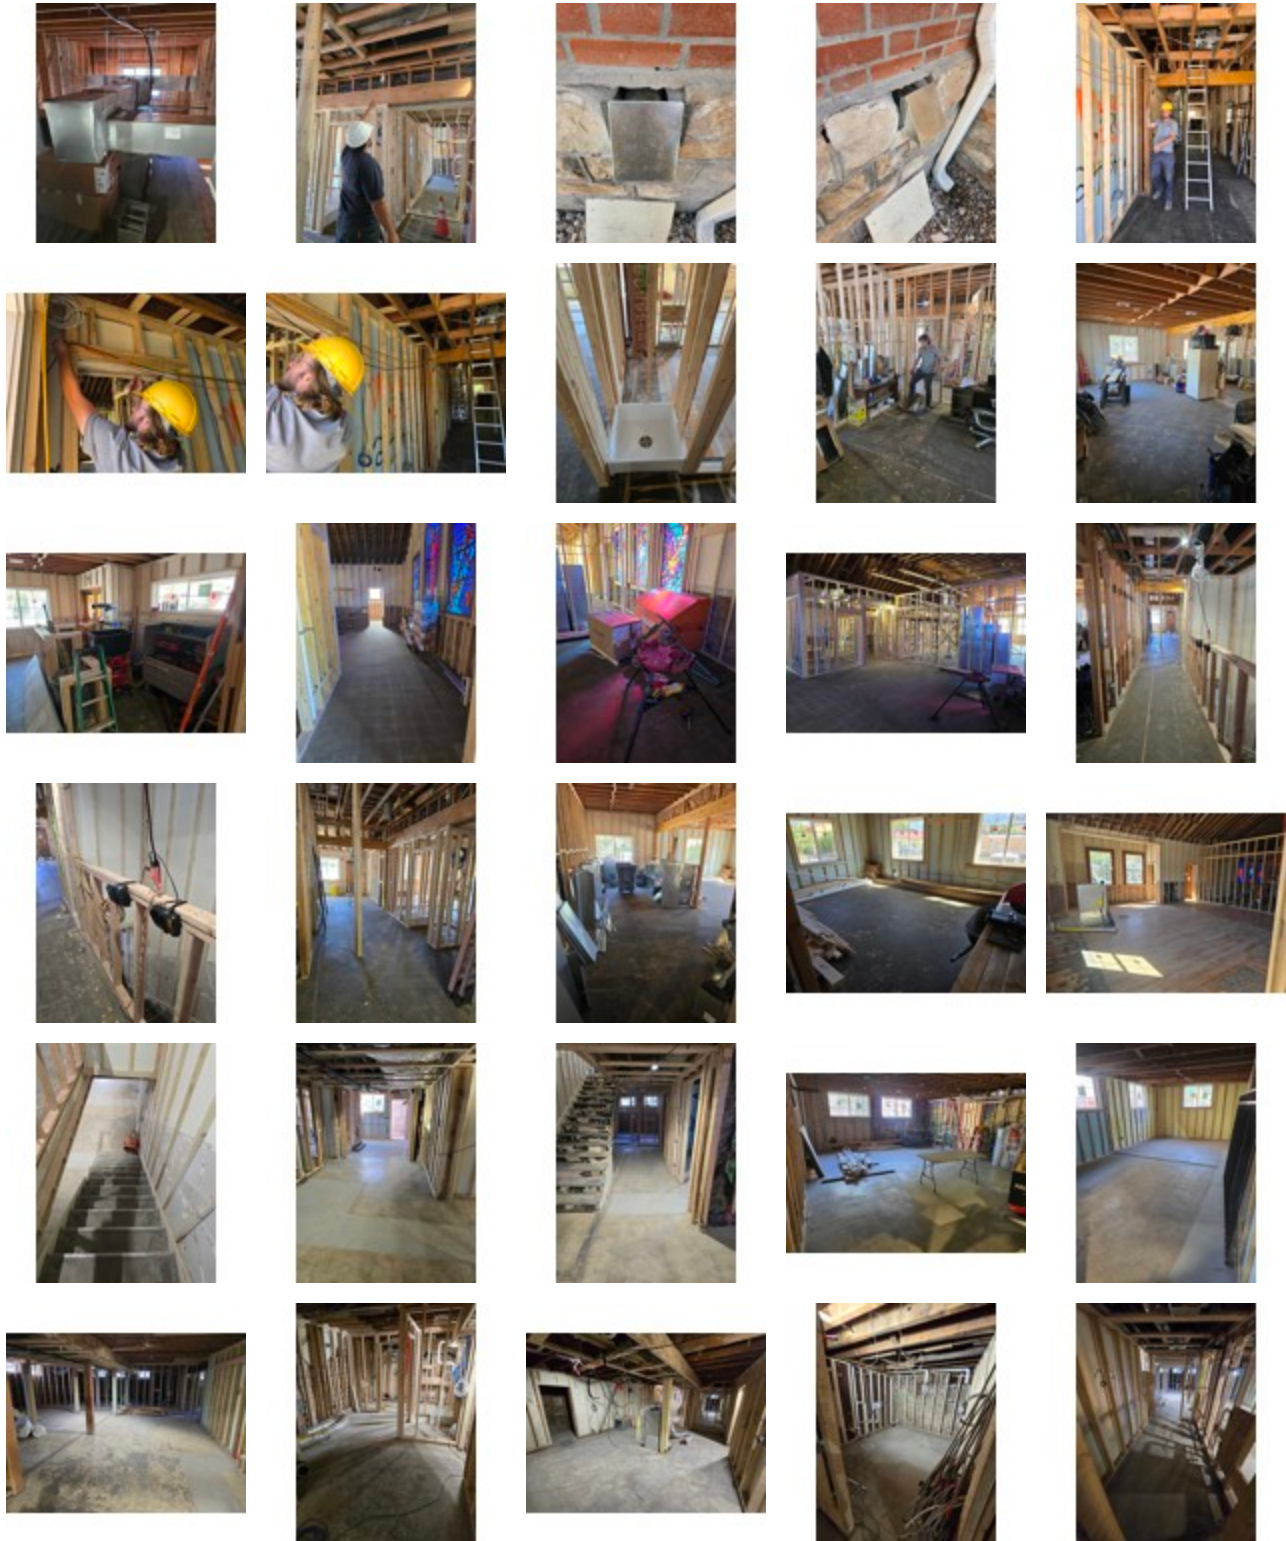

Jun 18, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7

-Began work in attic, installing duct runs and applying duct sealant to complete runs, met with superintendent on remaining

scope and timeline as they need to staff up and complete their scopes of work asap, cleaned up, left site at 4 pm

Weather Conditions:

Mostly sunny Thu, Jun 18, 2026, 9:35 AM



84°F
56°F

Wind: 16 mph
Humidity: 51%
Total Precip: 0"

Attachments: 15



Jun 17, 2026

Job: 2927 W Pikes Peak Ave

Title: American Electric

Added By: Marlowe Downey

Log Notes:

Arrived at 1:30

-Moved ceiling lights in utility closet and restroom

-Connected building ground to water line

Left at 5:00

Weather Conditions:

Mostly sunny Wed, Jun 17, 2026, 4:47 PM



97°F
72°F

Wind: 18 mph
Humidity: 28%
Total Precip: 0"

Attachments: 3



Jun 17, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 8:45

Continued working in attic applying duct sealant , installing transitions, delivered materials, cleaned up and left site at 4 pm

Weather Conditions:

Mostly sunny Wed, Jun 17, 2026, 9:17 AM



99°F

73°F

Wind: 17 mph

Humidity: 25%

Total Precip: 0"

Attachments: 4



Jun 17, 2026

Job: 2927 W Pikes Peak Ave

Title: Whitcomb Plumbing

Added By: Marlowe Downey

Log Notes:

Arrived at 6:50

- Completed main water hook up
- Scheduled CSU meter install, waiting for scheduling confirmation
- Installed mop sink in upper level utility closet

Left at 4:45

Weather Conditions:

Sunny Wed, Jun 17, 2026, 7:33 AM



92°F

62°F

Wind: 13 mph

Humidity: 36%

Total Precip: 0"

Attachments: 4



Jun 17, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site: Opened all exterior doors but the west side door, turned on all lights and fan, Opened most windows, performed perimeter sweep

-Supervising Whitcomb plumbers

-Completing full site clean up

-Organized all lumber and categorized with sizes as well

-Cleaned, shut down and locked entire site

-Dumpster caught fire at my fault, emptied watered down ash from grill into dumpster unthinkingly, fire department came out and put fire out (will be contacting dumpster service tomorrow)

Clocked out at 5:18

Weather Conditions:

Sunny Wed, Jun 17, 2026, 7:27 AM



97°F

Wind: 30 mph

64°F

Humidity: 24%

Total Precip: 0"

Attachments: 3



Jun 16, 2026

Job: 2927 W Pikes Peak Ave

Title: Whitcomb Plumbing

Added By: Marlowe Downey

Log Notes:

Arrived at 10:39

-Made material list for water hook up

Left at 10:50

Weather Conditions:

Mostly sunny Tue, Jun 16, 2026, 10:32 AM



86°F

48°F

Wind: 7 mph
Humidity: 47%
Total Precip: 0"

Attachments: 0

Jun 16, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:54

- Opened site: Unlocked upper level main door, upper level south door, and lower level entry door, turned on lights and completed perimeter sweep
- Cut unusable pipe sitting next to dumpster and threw away
- Assisted CWAM with vehicle relocation and moved box truck back to sit next to conex
- Continued site maintenance
- Assisted CWAM as needed
- Walked around site exterior and picked up trash
- Framed up walls dividing utility closet and bathroom in upper level with Casey
- Cleaned up and locked site

Left at 4:15

Weather Conditions:

Mostly sunny Tue, Jun 16, 2026, 7:47 AM



89°F

51°F

Wind: 10 mph
Humidity: 42%
Total Precip: 0"

Attachments: 2



Jun 16, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Marlowe opened site, pm work in office, set up workstation, supervision, scheduling, framed in janitor closet and mop sink per 205 changes, we will need some more 2x4 lumber to finish the soffits and chases through, spoke with the electrician and the CT Cabinet is lost in transit, they are working to locate it, they plan to install remaining electrical panels and devices next week, site cleaning, secured and closed site at 4:30 pm

Weather Conditions:

Sunny Tue, Jun 16, 2026, 12:00 AM

88°F

Wind: 9 mph



50°F

Humidity: 66%

Total Precip: 0"

Attachments:

11



Jun 16, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:10

-Set up equipment and began work in attic applying duct sealant and installing transitions, left site at 3:30 pm

Weather Conditions:

Mostly sunny Tue, Jun 16, 2026, 7:47 AM



89°F

Wind: 10 mph

51°F

Humidity: 42%

Total Precip: 0"

Attachments:

4



Jun 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 6:54

-Completed full exterior site check (all aspects within normality)

-Opened site (turned on lights, opened upper level main entry door and lower level entry door, opened some windows in upper level)

-Cleaned and organized site furthermore

Left site for brief other job maintenance at 8:40

Arrived back at 12:40

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 15, 2026, 6:57 AM



73°F

Wind: 9 mph

43°F

Humidity: 84%

Total Precip: 0"

Attachments: 0

Jun 15, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Marlowe opened site and inspected, set up workstation, supervision, scheduling, had review meeting with Summit fire, set up job refrigerator and microwave, met with owner John and Kelly's dad for a site walk, pm work, closed site at 3:30pm, finished the day at the office

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 15, 2026, 3:14 PM



Partly cloudy with isolated storms

75°F

Wind: 9 mph

43°F

Humidity: 85%

Total Precip: 0.06"

Attachments: 3



Jun 15, 2026

Job: 2927 W Pikes Peak Ave
Title: CWAM - HVAC
Added By: Marlowe Downey

Log Notes:

Arrived at 7:30

-Unloaded equipment and began work in upper level bathroom duct and attic applying duct sealant

-cut and installed ductwork in upper level

-Cleaning

-left site at 3 pm to get materials for the week

Weather Conditions:

Partly cloudy with showers Mon, Jun 15, 2026, 8:37 AM



77°F

47°F

Wind: 8 mph

Humidity: 89%

Total Precip: 0.01"

Attachments: 2



Jun 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp excavation

Added By: Casey Copley

Log Notes:

Loaded and exported debris pile in parking lot, cleaned up

Weather Conditions:

Partly cloudy with showers Sat, Jun 13, 2026, 12:00 AM



79°F

55°F

Wind: 7 mph

Humidity: 74%

Total Precip: 0.01"

Attachments: 0

Jun 12, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

-Opened site (unlocked doors, turned on lights, perimeter sweep and insured no unauthorized personnel)

-Supervising CWAM

Left at 7:12 to make delivery

Arrived back at 8:13

Weather Conditions:

Mostly sunny Fri, Jun 12, 2026, 6:51 AM



89°F

48°F

Wind: 14 mph

Humidity: 41%

Total Precip: 0"

Attachments: 0

Jun 12, 2026

Job: 2927 W Pikes Peak Ave
Title: CWAM - HVAC
Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

-Prepped for job

-Started hanging insulation around duct in lower level classroom

Weather Conditions:

Mostly sunny Fri, Jun 12, 2026, 7:06 AM



89°F

48°F

Wind: 14 mph

Humidity: 40%

Total Precip: 0"

Attachments: 6



Jun 11, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 6:55

-Opened site (unlocked doors, windows, job box, and turned on power)

-Assisted and supervised CWAM

-Homeless people vacated dumpster enclosure after arrival

-Assisted Casey with bathroom framing

-Demoed old ducting for summit fire personnel to access area

-Organized and buttoned up site further

-Cleaned up and locked site

Left at 4:00

Weather Conditions:

Sunny Thu, Jun 11, 2026, 6:48 AM



78°F

53°F

Wind: 21 mph

Humidity: 32%

Total Precip: 0"

Attachments: 0

Jun 11, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Casey Copley

Log Notes:

Arrived at 9 am, met with SHC team for fire piping coordination meeting, performed red lines for new design, left site at 4:15pm

Weather Conditions:

Sunny Thu, Jun 11, 2026, 3:34 PM



Sunny

74°F

Wind: 22 mph

Humidity: 76%

52°F

Total Precip: 0"

Attachments: 5



Jun 11, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7:05

-Began work in upper level bathroom fans, continued working on attic ducting, clean up, left site at 4 pm.

Weather Conditions:

Sunny Thu, Jun 11, 2026, 7:24 AM



77°F

Wind: 22 mph

Humidity: 33%

54°F

Total Precip: 0"

Attachments: 7



Jun 10, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 12:30

-Began work in middle upper level classroom, attic, and hallway

-Cleaned and swept up

Left at 3:50

Weather Conditions:

Mostly sunny Wed, Jun 10, 2026, 1:48 PM



89°F

58°F

Wind: 22 mph

Humidity: 42%

Total Precip: 0"

Attachments: 3



Jun 10, 2026

Job: 2927 W Pikes Peak Ave

Title: Rock and Roll Off

Added By: Marlowe Downey

Log Notes:

Arrived at 7:10

-Swapped dumpster for a new dumpster

Weather Conditions:

Mostly sunny Wed, Jun 10, 2026, 7:02 AM



88°F

59°F

Wind: 20 mph
Humidity: 41%
Total Precip: 0"

Attachments: 5



Jun 10, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 7:05

- Opened site (opened windows, turned on lights, and fans)
- Completely cleaned and organized interior and exterior
- Supervised CWAM
- Retrieved motor oil for Casey
- Locked all doors and windows as well as turning off lights

Left at 3:52

Weather Conditions:

Mostly sunny Wed, Jun 10, 2026, 7:02 AM



88°F

59°F

Wind: 20 mph
Humidity: 41%
Total Precip: 0"

Attachments: 0

Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Whitcomb Plumbing
Added By: Casey Copley

Log Notes:

Arrived at 7 am, set up, worked on condensation drains, relocated mop sink in janitors closet, got a materials list together, left site at 3 pm

Weather Conditions:

Partly cloudy with patchy blowing dust Tue, Jun 9, 2026, 4:46 PM



Partly cloudy with patchy blowing dust

85°F

59°F

Wind: 39 mph
Humidity: 91%
Total Precip: 0"



Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Opened site, site inspection, supervision, scheduling, verifications, continued re framing work with ownership team, site cleaning and organizing, met on site with Lee and Caleb to discuss the fire sprinkler system install and agreed to give summit fire a stop work order because the work is not accepted as it does not adhere to our contract, the installers stated that they saw the writing on the wall and were expecting me to tell them to stop as they did not like it either, assisted plumbers with rerouting the mop sink, clean up site, closed site at 5 pm

Weather Conditions:

Partly cloudy Tue, Jun 9, 2026, 4:31 PM



Partly cloudy

88°F


58°F

Wind: 27 mph

Humidity: 85%

Total Precip: 0"

Attachments: 14

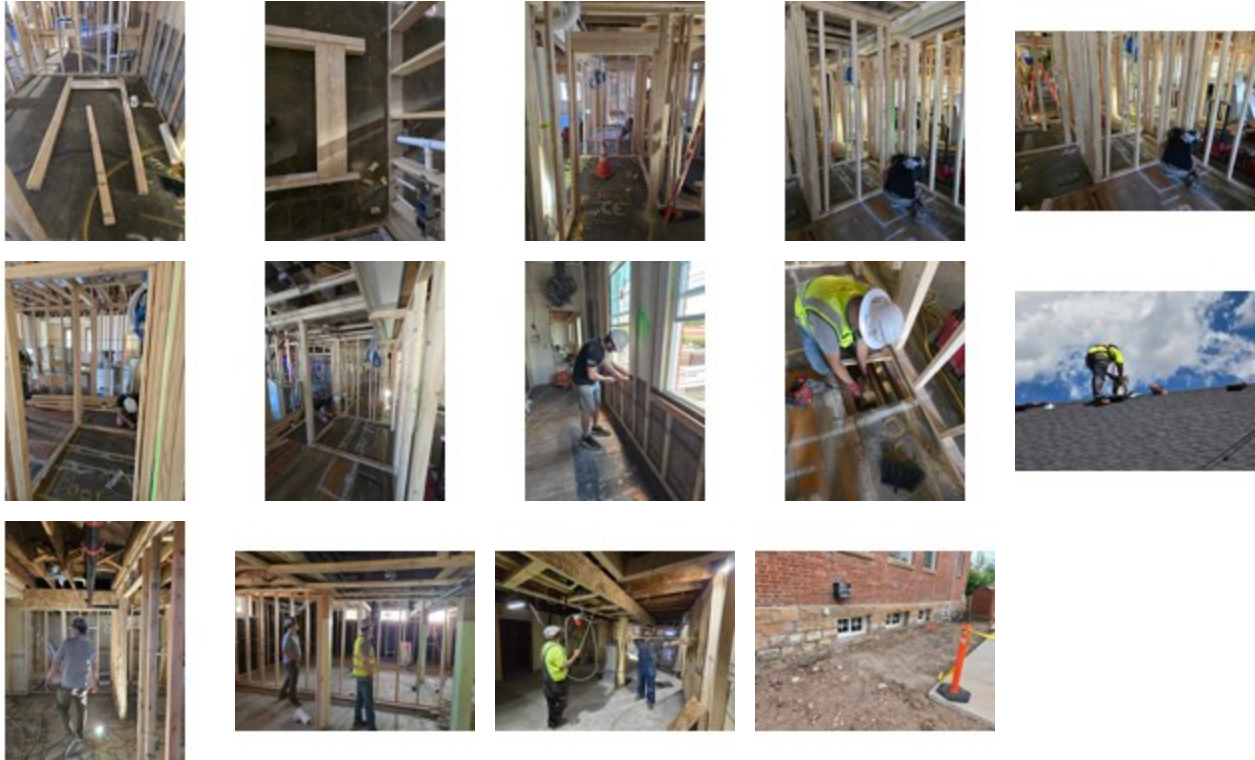

Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Thorp excavation
Added By: Casey Copley
Log Notes:

Loaded up equipment, he will be back on Friday to export the pile of debris in the parking lot and to power sweep.

Weather Conditions:

Partly cloudy Tue, Jun 9, 2026, 4:31 PM



Partly cloudy

88°F
58°F

Wind: 27 mph
Humidity: 85%
Total Precip: 0"

Attachments: 3



Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Summit fire
Added By: Casey Copley
Log Notes:

Arrived at 8 am, set up, began installing main line in lower level, the line is below 80" in many areas and is all surface mounted, casey had the installers stop installing as it is not what was agreed on and won't pass inspection, they agreed that the system design is not right and should be concealed pipe bird cage design so that the pipes can be in walls and ceiling, they cleaned up and loaded tools, left site at 4:45pm.

Weather Conditions:

Partly cloudy Tue, Jun 9, 2026, 4:31 PM

 Partly cloudy
88°F
58°F
Wind: 27 mph
Humidity: 85%
Total Precip: 0"

Attachments: 6



Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: David's window service
Added By: Casey Copley

Log Notes:

Arrived at 3 pm, installed lower level window, clean up, left site at 4:30,

Weather Conditions:

Partly cloudy Tue, Jun 9, 2026, 4:31 PM

 Partly cloudy
88°F
58°F
Wind: 27 mph
Humidity: 85%
Total Precip: 0"

Attachments: 3



Jun 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC

Added By: Casey Copley

Log Notes:

Arrived at 8 am, set up, continued working on attic ductwork, cut roof penetrations and dried in, installed concentric vents, cleaned up, left site at 4pm.

Weather Conditions:

Partly cloudy with patchy blowing dust Tue, Jun 9, 2026, 4:15 PM



Partly cloudy with patchy blowing dust

87°F

59°F

Wind: 40 mph

Humidity: 92%

Total Precip: 0"

Attachments: 3



Jun 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Steve opened site, set up, continued framing with ownership team, scheduling, supervision, site verifications, clean up, closed site at 5 pm

Weather Conditions:

Partly cloudy Mon, Jun 8, 2026, 12:00 AM



86°F

62°F

Wind: 12 mph

Humidity: 78%

Total Precip: 0"

Attachments: 5



Jun 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire protection

Added By: Casey Copley

Log Notes:

Arrived at 9 am, set up, unloaded and set up, marked up plans and planed out routing of pipe, they will need to re submit the plans because most of the routing will not work as drawn, left site at

Weather Conditions:

Partly cloudy Mon, Jun 8, 2026, 3:44 PM

 Partly cloudy

87°F

66°F

Wind: 18 mph

Humidity: 61%

Total Precip: 0"

Attachments: 5



Jun 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Whitcomb Plumbing

Added By: Casey Copley

Log Notes:

Site visit with superintendent and HVAC crew, discussed condensation lines, he will be back tomorrow to perform the remaining work,

Weather Conditions:

Partly cloudy Mon, Jun 8, 2026, 3:44 PM

 Partly cloudy

87°F

66°F

Wind: 18 mph

Humidity: 61%

Total Precip: 0"

Attachments: 2



Jun 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable services HVAC

Added By: Casey Copley

Log Notes:

Arrived at 7am, set up, continued installing ductwork in attic, sent fan submittals to Caleb for splice docs, walked with plumber on condensation drain routing, clean up, left site at 4pm

Weather Conditions:

Partly cloudy Mon, Jun 8, 2026, 3:44 PM

 Partly cloudy

87°F


66°F

Wind: 18 mph

Humidity: 61%

Total Precip: 0"

Attachments: 15



Jun 8, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 6:45am.

Unlocked, powered up, inspected, and opened the siteLeft @ 7am.

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 8, 2026, 6:44 AM



Partly cloudy with isolated storms

85°F
66°F

Wind: 16 mph

Humidity: 37%

Total Precip: 0"

Attachments: 0

Jun 5, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7:15am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am.

Poked my head from time to time to check on HVAC, see if the had any questions or concerns, and ensure the security of the site.

Ensured site was locked, windows were shut, and everything was secured.

Left @ 5:30pm.

Weather Conditions:

Partly cloudy with showers Fri, Jun 5, 2026, 5:22 PM



Partly cloudy with showers

77°F

56°F

Wind: 13 mph

Humidity: 41%

Total Precip: 0.08"

Attachments: 0

Jun 4, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM - HVAC

Added By: Marlowe Downey

Log Notes:

Arrived at 7

- Opened site lower door as well as upper south door

-Continued work on attic ducts

-Hung ducting above bathrooms in second level

-Cleaned all worked in areas

Left at 4:17

Weather Conditions:

Partly cloudy with isolated storms Thu, Jun 4, 2026, 7:35 AM



83°F

46°F

Wind: 8 mph

Humidity: 94%

Total Precip: 0"

Attachments: 3



Jun 4, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 7:30

-Met with CWAM, reviewed work load of the day and insured proper work environment

-Walked site interior and exterior for any unusual activity

Left at 7:45

Arrived back at 3:45

-Assisted CWAM with material retrieval within building

-Owners arrived on site with photographer to capture construction zone

-Closed all windows and insured all locked, turned off all lights, locked all doors

Left at 4:17

Weather Conditions:

Partly cloudy with isolated storms Thu, Jun 4, 2026, 7:35 AM



83°F

46°F

Wind: 8 mph

Humidity: 94%

Total Precip: 0"

Attachments: 0

Jun 3, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 11:07

-Assisted CWAM

-Completed legging under stained windows

-Organized and cleaned site

-Locked all doors, windows, and job box

Left at 4:17

Weather Conditions:

Mostly cloudy with thunderstorms Wed, Jun 3, 2026, 4:19 PM



74°F

50°F

Wind: 13 mph

Humidity: 88%

Total Precip: 0.15"

Attachments: 6



Jun 3, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Opened site, set up, supervision, scheduling, picked up splice plans and delivered to site for mechanical sub to verify so we can submit, lined Marlowe out for the day, left site at 12 pm,

Weather Conditions:

Partly cloudy with isolated storms Wed, Jun 3, 2026, 11:48 AM



Partly cloudy with isolated storms

77°F
50°F

Wind: 8 mph

Humidity: 88%

Total Precip: 0.07"

Attachments: 4



Jun 3, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC
Added By: Casey Copley

Log Notes:

Arrived at 8 am, set up, continued installing ductwork in attic, ran short on 10x16 ductwork, they said it will take a few days to get it in so they won't be able to get their inspection until mid week next week, Cleaned up and left at 4:00

Attachments: 7



Jun 2, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Set up, site inspection, supervision, continued installing backing with owners, cleaning, site verifications, scheduling, met with shad sail engineer and Lee, closed site at 5 pm

Weather Conditions:

Mostly cloudy with showers Tue, Jun 2, 2026, 4:31 PM



Mostly cloudy with showers

68°F

Wind: 13 mph

Humidity: 98%

52°F

Total Precip: 0.01"

Attachments: 8



Jun 2, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC
Added By: Casey Copley

Log Notes:

Arrived at 7am, set up, continued installing ducting in attic

Weather Conditions:

Mostly cloudy with showers Tue, Jun 2, 2026, 4:31 PM



Mostly cloudy with showers

68°F

Wind: 13 mph

52°F

Humidity: 98%

Total Precip: 0.01"

Attachments: 3



Jun 1, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at around 10:40

-Organized lumber to one location

-Pulled all nails out of scrap boards with John the owner

-Assisted Casey

-Once Casey left, continued instruction to both John and Luke of backing installment for bathrooms

-Had conflict with 2 CWAM members, Anthony and Tristian. Informed Anthony in a professional and respectful way teasing

and hazing with anyone whilst owners are in the building is unacceptable and unprofessional (got the response: your not my dad)

-Cleaned upper level and well as partial lower

-Assisted CWAM

-Organized and cleaned up job box and surrounding area as well as temp office space

-Locked all doors and windows

Left at around 4:15

Weather Conditions:

Partly cloudy with thunderstorms Mon, Jun 1, 2026, 5:29 PM



81°F

52°F

Wind: 18 mph

Humidity: 86%

Total Precip: 0.01"

Attachments: 7



Jun 1, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Steve opened site, picked up tools and supplies from shop and delivered to site, unloaded and set up, continued installing backing an nailers throughout with owner John team and Marlowe, scheduling, site verifications, installed corner post at staircase to lower level,

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 1, 2026, 10:15 AM



80°F

52°F

Wind: 12 mph

Humidity: 86%

Total Precip: 0.01"

Attachments: 0

Jun 1, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable Services (HVAC)

Added By: Casey Copley

Log Notes:

Arrived at 8 am, set up, continued working on attic supply and return ducting,

Weather Conditions:

Partly cloudy with isolated storms Mon, Jun 1, 2026, 10:15 AM



80°F

52°F

Wind: 12 mph

Humidity: 86%

Total Precip: 0.01"

Attachments: 0

May 28, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit fire

Added By: Casey Copley

Log Notes:

Arrived at 11 am, pipe fitters walked site, red lined plans for their engineers to update drawings/ submittal, encountered a few routing obstacles for main line and FDC controls, they left site at 3 pm to go to the office to work through the routing and design with their team

Weather Conditions:

Mostly cloudy with showers Thu, May 28, 2026, 3:35 PM



Mostly cloudy with showers

75°F

49°F

Wind: 13 mph

Humidity: 100%

Total Precip: 0.09"

Attachments: 6



May 28, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable Solutions (HVAC)

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am, set up, continued working on attic ducting above classrooms 204 205 206, began removal of temporary heating units, removed red lines of mechanical vent ducting for engineers splice, had larger crew show up to do a pre walk for work to be completed on Monday and Tuesday, clean up, left site at

Weather Conditions:

Partly cloudy with showers Thu, May 28, 2026, 7:05 AM



Partly cloudy with showers

71°F


49°F

Wind: 12 mph

Humidity: 100%

Total Precip: 0.07"

Attachments: 17



May 28, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.
Unlocked, powered up, inspected, and opened the site.
Left @ 7:15am.

Weather Conditions:

Partly cloudy with showers Thu, May 28, 2026, 7:05 AM



Partly cloudy with showers

71°F

49°F

Wind: 12 mph

Humidity: 100%

Total Precip: 0.07"

Attachments: 0

May 27, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 9:35

Weather Conditions:

Mostly cloudy with isolated storms Wed, May 27, 2026, 9:37 AM



62°F

51°F

Wind: 9 mph

Humidity: 93%

Total Precip: 0.2"

Attachments: 0

May 27, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Casey Copley

Log Notes:

Arrived at 9 am, met with Lee and Casey and discussed submittals and schedule, their most recent submittal was rejected again, they do not believe they will make the new deadline, they will be back tomorrow to work on red line and routing and update me on scheduling.

Weather Conditions:

Mostly cloudy with showers Wed, May 27, 2026, 4:33 PM



Mostly cloudy with showers

58°F

51°F

Wind: 12 mph

Humidity: 93%

Total Precip: 0.2"

Attachments: 2



May 27, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Supervision, scheduling, site verifications, worked with ownership team on wall backing, met with Lee and Summit fire and discussed submissions and scheduling, they do not think they will meet the deadline, they will be back tomorrow to do some redline work and discuss routing and schedule, got approval from ownership team to allow surface mounting, met with Lee on framing changes, cleaning, closed site at 4:30 pm

Weather Conditions:

Mostly cloudy with showers Wed, May 27, 2026, 4:33 PM



Mostly cloudy with showers

58°F

Wind: 12 mph

Humidity: 93%

51°F Total Precip: 0.2"

Attachments: 5



May 27, 2026


Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC
Added By: Casey Copley

Log Notes:

Arrived at 8:45 am, set up, finished lower level work based on inspectors comments, had inspection on lower level heat and vent (HV) and passed, waiting on splice from engineer for upper level to pass, worked on attic ducting, remove rectangle ducting from attic,

Weather Conditions:

Mostly cloudy with scattered showers Wed, May 27, 2026, 8:48 AM



60°F
50°F

Wind: 11 mph
Humidity: 100%
Total Precip: 0.12"

Attachments: 3



May 27, 2026


Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.
Unlocked, powered up, inspected, and opened the site.
Left @ 7am.

Weather Conditions:

Mostly cloudy with scattered showers Wed, May 27, 2026, 6:48 AM



59°F
49°F

Wind: 12 mph
Humidity: 82%
Total Precip: 0.07"

Attachments: 0

May 26, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7:15am.

Set up and continued with lower level rough in.

Weather Conditions:

Mostly cloudy with isolated storms Tue, May 26, 2026, 8:02 AM



Mostly cloudy with isolated storms

71°F
51°F

Wind: 22 mph

Humidity: 75%

Total Precip: 0.04"

Attachments: 3



May 26, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 8am.

Unlocked, powered up, inspected, and opened the site.

Discussed HVAC plan with Manny (lower level rough inspection today).

Left @ 8:15am.

Weather Conditions:

Mostly cloudy with isolated storms Tue, May 26, 2026, 8:02 AM



Mostly cloudy with isolated storms

71°F
51°F

Wind: 22 mph

Humidity: 75%

Total Precip: 0.04"

Attachments: 0

May 22, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 1:30

-Completed blocking with John the owner

-Supervised road workers

-Swept building

-Organized building

- Put up caution tape on side walk
- Delivered steel hangers inside
- Took portable WiFi
- Unloaded tools from truck into building
- Insured all windows and doors are locked
- Unplugged all cords
- Locked job box

Left at 3:57

Weather Conditions:

Partly cloudy with chance of storms Fri, May 22, 2026, 3:52 PM



61°F

40°F

Wind: 10 mph

Humidity: 82%

Total Precip: 0.06"

Attachments:

19



May 21, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Opened site, site inspection, set up, pm work and project coordination with caleb before he leaves for a vacation, site verifications, scheduling, supervision, worked on wall backing, cleaning, closed site at 5pm

Weather Conditions:

Mostly cloudy Thu, May 21, 2026, 12:00 AM



66°F
41°F

Wind: 16 mph
Humidity: 94%
Total Precip: 0"

Attachments: 0

May 21, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable solutions HVAC

Added By: Casey Copley

Log Notes:

Arrived at 7am, set up, installed riser ducting on restroom fans, installed dryer venting, finished line set work, had HI (lineset) inspection and passed, began installing condensation sleeves, finished water heater venting and roof penetrations, had inspection the inspector wants the manual uploaded before he can complete the inspection, cleaned up, left site at 5pm

Weather Conditions:

Partly cloudy with isolated storms Thu, May 21, 2026, 7:07 AM



Partly cloudy with isolated storms

66°F
41°F

Wind: 12 mph
Humidity: 93%
Total Precip: 0"

Attachments: 14



May 20, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Supervision, scheduling, site verifications, met with Caleb and worked through egress and framing changes for as build drawings, worked with ownership team on demo of wall for ductwork and installed wall backing for wall lvs, repaired floor joists, scheduled roofer to install boot on roof penetration, scheduled BSP inspection to discuss egress and omitting exterior door in classroom 205, cleaning, secured site, left at 6:30pm, CWAM closed site at 7:30pm,

Weather Conditions:

Cloudy with rain Wed, May 20, 2026, 12:00 AM



53°F

37°F

Wind: 5 mph

Humidity: 96%

Total Precip: 0.5"

Attachments: 7



May 20, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable solutions HVAC

Added By: Casey Copley

Log Notes:

Arrived at 8am, set up, installed pads for condensing units, worked on linesets and insulation, core drilled for dryer vent, installed water heater venting in wall and roof penetration, clean up, closed site at 7:30pm

Weather Conditions:

Cloudy with rain Wed, May 20, 2026, 12:00 AM



53°F


37°F

Wind: 5 mph

Humidity: 96%

Total Precip: 0.5"

Attachments: 20

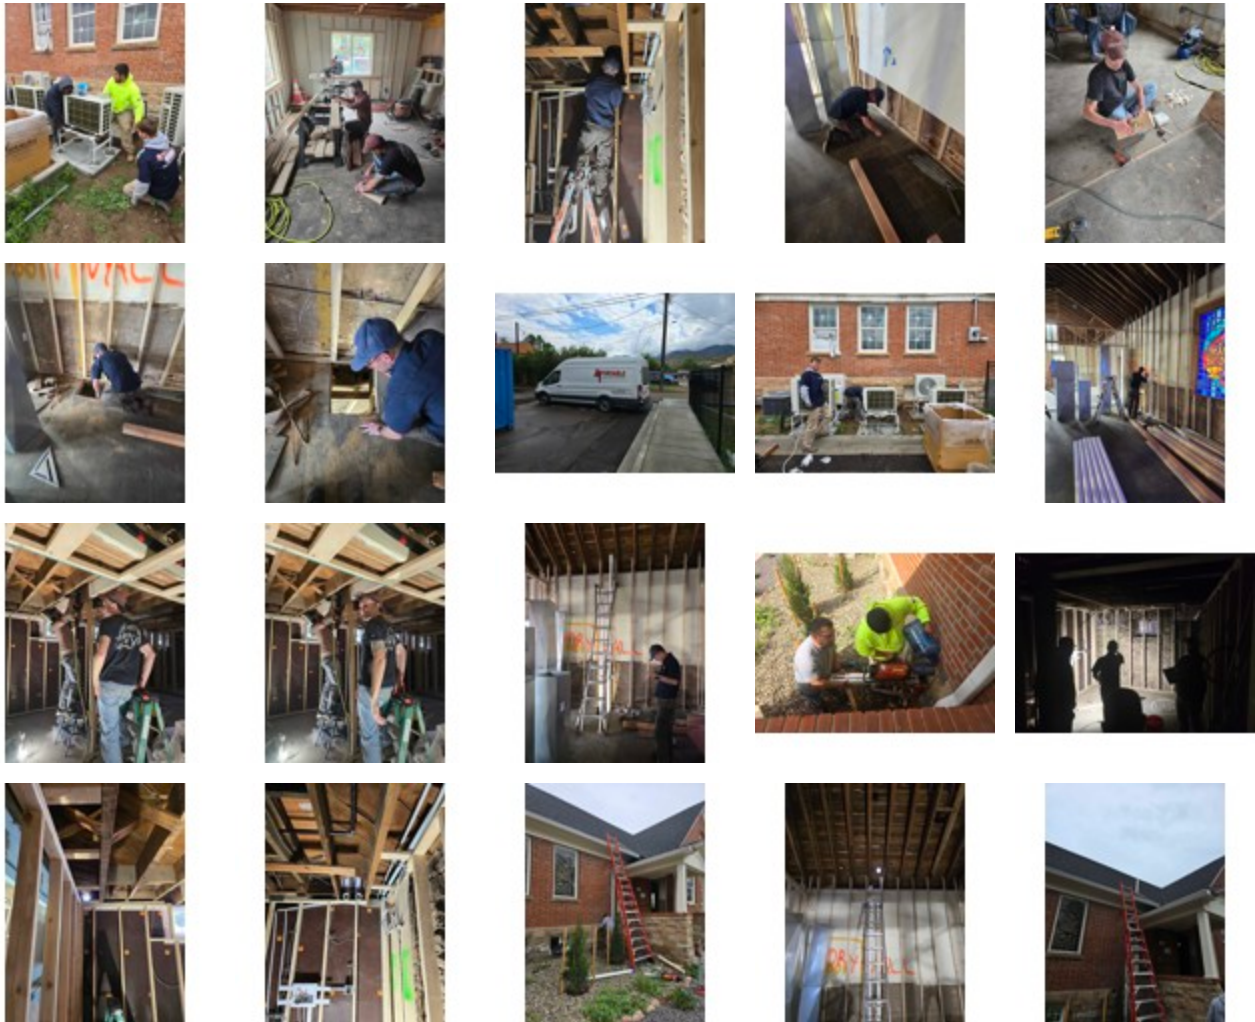

May 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.
Unlocked, powered up, inspected, and opened the site.
Left @ 7:15am.

Weather Conditions:

Mostly cloudy with showers Wed, May 20, 2026, 6:48 AM



Mostly cloudy with showers

57°F
39°F

Wind: 11 mph
Humidity: 98%
Total Precip: 0.6"

Attachments: 0

May 19, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up and continued with mechanical rough, worked on line sets and condensing units, changed out flex ducting to approved ducting, had HI rough inspection, got a partial and need to address inspectors comments, called for re inspection for Wednesday, cleaned up, left site at 5 pm

Weather Conditions:

Mostly cloudy with slight chance of light wintry mix Tue, May 19, 2026, 7:01 AM



Mostly cloudy with slight chance of light wintry mix

53°F
36°F

Wind: 12 mph

Humidity: 92%

Total Precip: 0.13"

Attachments:

24



May 19, 2026

Job:

2927 W Pikes Peak Ave

Title:

Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Weather Conditions:

Mostly cloudy with slight chance of light wintry mix Tue, May 19, 2026, 7:01 AM



Mostly cloudy with slight chance of light wintry mix

53°F

36°F

Wind: 12 mph

Humidity: 92%

Total Precip: 0.13"

Attachments: 0

May 18, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:45am

Returned @ 3:45pm.

Talked with Shane about water heater vent placement.

Supervised mechanical work.

Left @ 5:15pm

Weather Conditions:

Mostly cloudy with chance of light wintry mix Mon, May 18, 2026, 6:44 AM



Mostly cloudy with chance of light wintry mix

48°F

35°F

Wind: 25 mph

Humidity: 96%

Total Precip: 0.3"

Attachments: 2



May 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7:15am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:30am.

Weather Conditions:

Partly cloudy with isolated storms Fri, May 15, 2026, 7:22 AM



Partly cloudy with isolated storms

81°F
55°F

Wind: 9 mph
Humidity: 48%
Total Precip: 0"

Attachments: 0

May 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Steve opened site, arrived at 9 am, supervision, scheduling, pm work, spoke with excavator and he stated that they need to dig the pipe back up at the foundation in order to do an adjustment, they will be back tomorrow to perform this, they also plan to pour back the curb and gutter, spoke with mechanical team and they said that the dryer vent and the water heater venting was not part of their scope, I will review the subcontractor agreements to see if it is in their or the plumbers scope, met with radon installer for re routing removed pipe, closed site at 430 pm, worked at office for rest of the day

Weather Conditions:

Partly cloudy with isolated storms Thu, May 14, 2026, 4:50 PM



Partly cloudy with isolated storms

82°F
65°F

Wind: 24 mph
Humidity: 35%
Total Precip: 0"

Attachments: 4



May 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Summit fire
Added By: Casey Copley

Log Notes:

Arrived at 9am, unloaded pipe and materials, walked site with Casey, left at 1 pm

Weather Conditions:

Partly cloudy with isolated storms Thu, May 14, 2026, 4:50 PM



Partly cloudy with isolated storms

82°F
65°F

Wind: 24 mph
Humidity: 35%
Total Precip: 0"

Attachments: 4



May 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Set up and continued with rough in, installed fan venting, core drilled exterior walls, called for in wall and floor rough inspection for tomorrow, left site at 4:15 pm

Weather Conditions:

Partly cloudy with isolated storms Thu, May 14, 2026, 1:06 PM



Partly cloudy with isolated storms


82°F
57°F

Wind: 20 mph

Humidity: 54%

Total Precip: 0"

Attachments: 8



May 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am.

Returned @ 1am.

Looked over site.

Left @ 1:15am.

Weather Conditions:

Partly cloudy with isolated storms Thu, May 14, 2026, 1:06 PM



Partly cloudy with isolated storms

82°F

57°F

Wind: 20 mph

Humidity: 54%

Total Precip: 0"

Attachments: 1



May 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Marlowe Downey

Log Notes:

Arrived at 12:30

-Reviewed job site planning

-Prepared for inspection and gathered permit

-Conducted inspection (results will come soon)

Left at around 1:15

Weather Conditions:

Partly cloudy with showers Wed, May 13, 2026, 4:49 PM



77°F

50°F

Wind: 14 mph

Humidity: 52%

Total Precip: 0.02"

Attachments: 0

May 13, 2026

Job: 2927 W Pikes Peak Ave

Title: CWAM

Added By: Marlowe Downey

Log Notes:

Arrived at 10:30

-Began job site planning of the day

-Rented machinery to cut hole into lower level bathroom wall to exterior

-Cut hole into lower level wall using a red head style bolt to secure core drill machine

Left at 4:20

Weather Conditions:

Partly cloudy with showers Wed, May 13, 2026, 4:49 PM

77°F

Wind: 14 mph

Humidity: 52%



50°F

Total Precip: 0.02"

Attachments: 5



May 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:53

- Completed a perimeter sweep
- Opened job
- Swept the whole building
- cut blocking for rooms 202, 203, and two bathrooms
- Started on hole in search of city water tap
- Assisted CWAM with print reading
- Went to other job site and filled three water jugs for CWAM to cut hole in lower level concrete
- Met with summit fire tech and reviewed site (Fire inspection is scheduled for today)

Left at 12:50

Weather Conditions:

Partly cloudy with showers Wed, May 13, 2026, 7:03 AM



76°F

Wind: 17 mph

46°F

Humidity: 64%

Total Precip: 0.01"

Attachments: 0

May 12, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 8:30

- Dropped off electric concrete mixer, 2 man auger, and 12" bit
- Ran extension cord through the window for the mixer
- Owners arrived at 9:01
- Filled 3 water jugs from other site and delivered at job

Left at 9:40

Arrived back at 12:34

- Owners tasked me with picking up more concrete as well as picking up a special T40 bit
- Worked on nailers with John
- Started on backing in room 202

-Cleaned up and organized tools
-Swept floors
Left at 4:13
-Delivered rented machinery at 4:25

Weather Conditions:

Mostly sunny Tue, May 12, 2026, 8:53 AM



83°F

51°F

Wind: 11 mph
Humidity: 43%
Total Precip: 0"

Attachments: 0

May 12, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.
Unlocked, powered up, inspected, and opened the site.

Weather Conditions:

Mostly sunny Tue, May 12, 2026, 12:00 AM



79°F

55°F

Wind: 17 mph
Humidity: 39%
Total Precip: 0"

Attachments: 0

May 11, 2026

Job: 2927 W Pikes Peak Ave
Title: Colorado Water and Mold
Added By: Marlowe Downey

Log Notes:

Arrived at 7:00
-Set up work site
-Cleaned attic area
-Manny set up his computer and added in all StreamHome members
-Duct work in attic and bathroom fans in upper and lower level
-Cleaned up work areas

Weather Conditions:

Sunny Mon, May 11, 2026, 9:01 AM



80°F

41°F

Wind: 9 mph
Humidity: 84%
Total Precip: 0"

Attachments: 6



May 11, 2026

Job: 2927 W Pikes Peak Ave
Title: Whitcomb Plumbing Insulation
Added By: Marlowe Downey
Log Notes:

Arrived at 7:30

-Work on lower level insulation in bathrooms and kitchen

-Finished area and cleaned up work space

Left at 2:35

Weather Conditions:

Sunny Mon, May 11, 2026, 7:45 AM



80°F


42°F

Wind: 9 mph

Humidity: 84%

Total Precip: 0"

Attachments: 8



May 11, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 7:15

- Went over plan with CWAM
- Opened front door for traffic of the plumbing insulators
- Sweeping all areas and organizing material
- Insuring fluid work with CWAM
- Supervising Plumbing insulators
- Noticed 2 homeless people camping in tent in the dumpster enclosure at 9:45 informed them they must clean up and leave and to never come back or law will be involved
- Had CWAM tighten lower furnace gas connection due to small gas leak
- CWAM is scheduled to come tomorrow and finish all bathroom fans as well as start on attic ductwork
- Plumbing insulation is scheduled to continue tomorrow
- Assisted CWAM with blueprint reading
- Cleaned up area, closed all windows, turned off all lights
- Locked site and completed one final perimeter sweep (threw away shoes left at door as well)

Left at 3:53

Weather Conditions:

Sunny Mon, May 11, 2026, 6:15 AM



81°F

47°F

Wind: 9 mph

Humidity: 73%

Total Precip: 0"

Attachments: 8



May 11, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am

Weather Conditions:

Sunny Mon, May 11, 2026, 6:15 AM

Wind: 9 mph



Sunny

81°F

47°F

Humidity: 73%

Total Precip: 0"

Attachments: 0

May 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp Excavation

Added By: Marlowe Downey

Log Notes:

Arrived at 7:05

-Prepped for the work day

-Resumed compaction

Weather Conditions:

Mostly sunny Fri, May 8, 2026, 7:09 AM



68°F

43°F

Wind: 16 mph

Humidity: 64%

Total Precip: 0"

Attachments: 1



May 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Colorado Water and Mold

Added By: Marlowe Downey

Log Notes:

Arrived at 6:59

-Prepared site

-Resuming work on bathroom fans

Weather Conditions:

Partly cloudy Fri, May 8, 2026, 6:55 AM



70°F

42°F

Wind: 10 mph

Humidity: 72%

Total Precip: 0"

Attachments: 1



May 8, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 6:57

-Opened job, turned on all lights and power, preformed perimeter sweep

-Resuming framing work

Weather Conditions:

Partly cloudy Fri, May 8, 2026, 6:55 AM



70°F

42°F

Wind: 10 mph

Humidity: 72%

Total Precip: 0"

Attachments: 0

May 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Opened site, site inspection, set up workstation, pm work, supervision, scheduling, worked through Summit fire contracts and current situation, received unapproved change order from Thorp for road work/tap, worked until 7:30pm,

Weather Conditions:

Mostly sunny Thu, May 7, 2026, 12:00 AM



67°F

29°F

Wind: 13 mph

Humidity: 89%

Total Precip: 0"

Attachments: 0

May 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 3:30pm.

Excavators passed second compaction test and opened up the road.

Cleaned up, locked up, powered down, and closed the site @ 4:45pm.

Weather Conditions:

Partly cloudy with snow showers Thu, May 7, 2026, 4:37 PM



Partly cloudy with snow showers

63°F

27°F

Wind: 12 mph

Humidity: 93%

Total Precip: 0"

Attachments: 0

May 7, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:


Arrived @ 8:15am, set up, continued working on exaust ducting, met with PPRBD inspector for consultation on routing and flex ducting, removed non UL listed flex connections, clean up left at 4pm

Weather Conditions:

Mostly sunny Thu, May 7, 2026, 8:52 AM

 Mostly sunny
64°F
29°F
Wind: 10 mph
Humidity: 89%
Total Precip: 0"

Attachments: 11

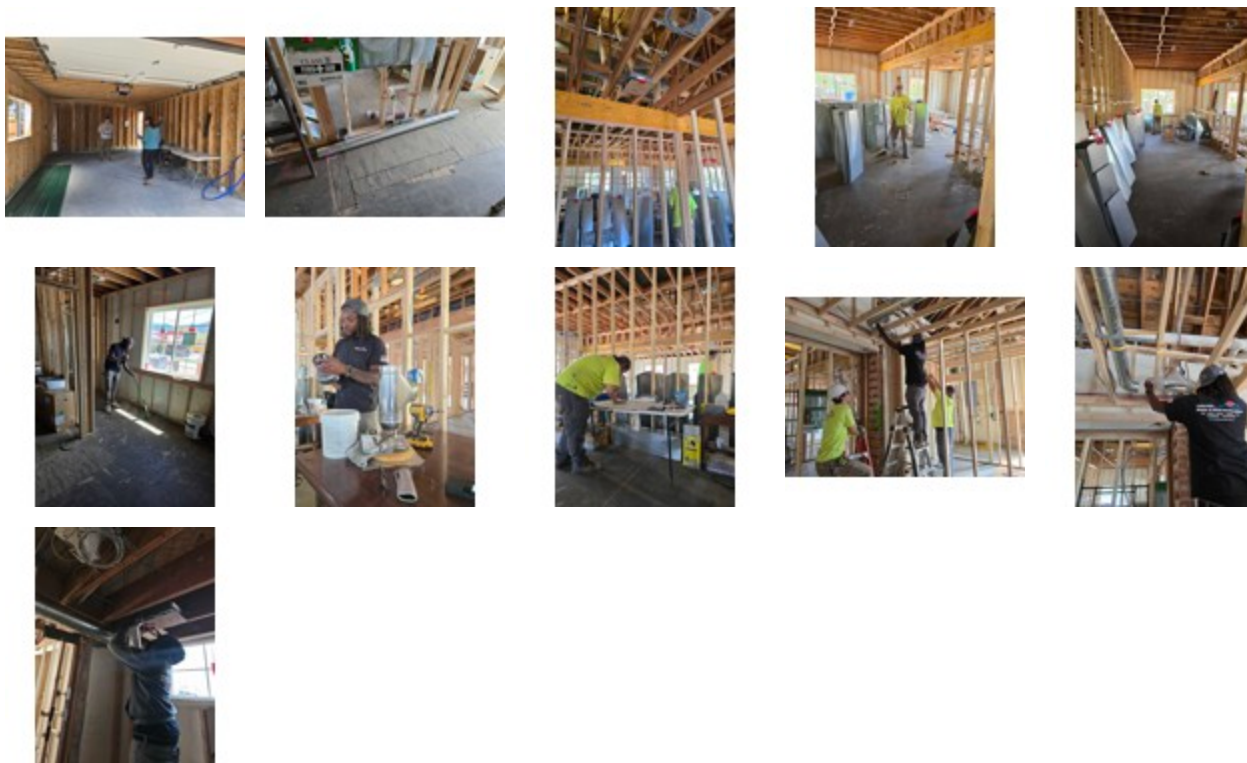

May 7, 2026

Job: 2927 W Pikes Peak Ave
Title: Thorpe Excavation
Added By: Stephen Michaels

Log Notes:

Arrived @ 8am.

Set up and began installing 90° elbow inside the wall on the lower level, pulled soil from hole and re backfilled and compacted, had compaction test, left site at 4:30 pm

Weather Conditions:

Mostly sunny Thu, May 7, 2026, 8:52 AM

 Mostly sunny
64°F
29°F
Wind: 10 mph
Humidity: 89%
Total Precip: 0"

Attachments: 8



May 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Summit Fire

Added By: Stephen Michaels

Log Notes:

Arrived @ 8:15am.

Looked over site. I showed John the two places that they installed ahead of the soffits that needed to be dropped down. He said they should be inspection ready by Friday or Monday.

Left @ 8:45am.

Weather Conditions:

Mostly sunny Thu, May 7, 2026, 8:37 AM

 Mostly sunny
59°F
24°F
Wind: 8 mph
Humidity: 92%
Total Precip: 0"

Attachments: 4



May 7, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 8:15am.

Inspected site.

Weather Conditions:

Mostly sunny Thu, May 7, 2026, 8:21 AM



Mostly sunny

65°F

28°F

Wind: 8 mph

Humidity: 96%

Total Precip: 0"

Attachments: 0

May 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 8:38

Weather Conditions:

Mostly cloudy with snow showers Wed, May 6, 2026, 8:35 AM



37°F

29°F

Wind: 15 mph

Humidity: 95%

Total Precip: 0.32"

Attachments: 0

May 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable services HVAC

Added By: Casey Copley

Log Notes:

Arrived at 8:30 am, set up, assembled venting ductwork, began installing and encountered routing issues, we attempted to re-route but were unsuccessful as structure and meps are in the way, they are sending an RFI on it, clean up left site at 4pm

Weather Conditions:

Mostly cloudy with light wintry mix Wed, May 6, 2026, 4:35 PM



Mostly cloudy with light wintry mix

51°F

28°F

Wind: 8 mph

Humidity: 95%

Total Precip: 0.35"

Attachments: 7



May 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp excavation

Added By: Casey Copley

Log Notes:

picked up steel plates, informed me that they did fail the compaction test and will be required to dig up the road base and start over on backfills and compaction, they will be back tomorrow to get to work on it.

Weather Conditions:

Mostly cloudy with light wintry mix Wed, May 6, 2026, 4:35 PM



Mostly cloudy with light wintry mix

51°F

28°F

Wind: 8 mph

Humidity: 95%

Total Precip: 0.35"

Attachments: 3



May 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Opened site at 7am, set up workstation, site inspection, there was a homeless man sleeping on the porch on 30th st side, it appears that people have been skateboarding on the front entry ramp wall cap, it is slightly damaged, scheduling supervision, site verifications and working through routing issues with mechanical, pm work, cleaning, closed site at 4:30pm

Weather Conditions:

Mostly cloudy with wintry mix Wed, May 6, 2026, 3:51 PM



Mostly cloudy with wintry mix

37°F

29°F

Wind: 15 mph

Humidity: 93%

Total Precip: 0.34"



May 5, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Opened site at 7 am, met with ownership team, relocated concrete inside playground, set up, cut and installed soni tubes, mixed concrete and filled tubes until we got rained out, supervision, scheduling, spoke with Caleb and he informed me that Summit Fire has not received plan approval so he investigated and found that their license is suspended and their insurance is expired, we are working to get answers, I did inform the owners of this issue, site verifications for HVAC crew, met with pipeline inspector, he is concerned that Thorp will not meet the compaction required for the road base and said he may require them to take additional classes to educate them on city service, met with Jonna for bank draw inspection, cleaned and returned rental equipment to Bill's, left site at 12:30 pm, Steve closed site at 4:30 pm

Weather Conditions:

Cloudy with light wintry mix Tue, May 5, 2026, 12:00 AM



48°F

32°F

Wind: 7 mph

Humidity: 96%

Total Precip: 0.17"

Attachments:

16



May 5, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable services HVAC
Added By: Casey Copley

Log Notes:

Arrived at 8 am, set up, worked on exhaust fans and ducting in lower level, cleaned up and left site at 4 pm

Weather Conditions:

Cloudy with light wintry mix Tue, May 5, 2026, 12:00 AM



48°F

32°F

Wind: 7 mph

Humidity: 96%

Total Precip: 0.17"

Attachments: 5



May 4, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 10:30

-Delivered two man auger with 12"blade, electric concrete mixer with stand from Bills rentals (return time is 11:00 tomorrow)

Left at 10:38

Weather Conditions:

Mostly cloudy with isolated storms Mon, May 4, 2026, 10:46 AM



73°F

Wind: 13 mph

47°F

Humidity: 63%

Total Precip: 0.01"

Attachments: 0

May 4, 2026

Job: 2927 W Pikes Peak Ave

Title: Iron mountain porta potty

Added By: Casey Copley

Log Notes:

Performed cleaning maintenance on porta potty

Weather Conditions:

Mostly cloudy with isolated storms Mon, May 4, 2026, 5:31 PM



Mostly cloudy with isolated storms

69°F

Wind: 20 mph

47°F

Humidity: 62%

Total Precip: 0.06"

Attachments: 1



May 4, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Site inspection, scheduling, supervision, worked with ownership team with playground equipment layout and digging holes, closed site at 5:40 pm

Weather Conditions:

Mostly cloudy with isolated storms Mon, May 4, 2026, 5:31 PM



Mostly cloudy with isolated storms

69°F

47°F

Wind: 20 mph

Humidity: 62%

Total Precip: 0.06"



May 4, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am.

Weather Conditions:

Mostly cloudy with isolated storms Mon, May 4, 2026, 7:01 AM



Mostly cloudy with isolated storms

71°F
46°F

Wind: 14 mph

Humidity: 66%

Total Precip: 0.01"

Attachments: 3



May 1, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Picked up lumber, supervision, scheduling, site inspection, met with Kelly at 10:30 am, worked together and framed soffit in lower level, installed nailers for drywall, clean up, closed site at 5:15pm

Weather Conditions:

Partly cloudy with light wintry mix Fri, May 1, 2026, 12:00 AM



55°F
33°F

Wind: 5 mph

Humidity: 99%

Total Precip: 0.04"

Attachments: 4



May 1, 2026

Job: 2927 W Pikes Peak Ave
Title: Thorpe Excavation
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Set up, warmed up excavators. Plan is to begin and hopefully finish backfill today.

Making good progress with backfill.

Weather Conditions:

Partly cloudy with slight chance of wintry mix Fri, May 1, 2026, 7:09 AM

Wind: 8 mph

 Partly cloudy with slight chance of wintry mix

55°F
33°F

Humidity: 97%
Total Precip: 0.03"

Attachments: 18



May 1, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Weather Conditions:

Partly cloudy with slight chance of wintry mix Fri, May 1, 2026, 6:54 AM

 Partly cloudy with slight chance of wintry mix

55°F
33°F

Wind: 8 mph
Humidity: 97%
Total Precip: 0.03"

Attachments: 2



Apr 30, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Arrived @ 8am.

Set up and removed steel plates from hole.

Pumped abandoned storm drain with flow fill. Needs to set up for 24 hours. Will return tomorrow morning to begin backfill.

Weather Conditions:

Cloudy with light wintry mix likely Thu, Apr 30, 2026, 8:12 AM



Cloudy with light wintry mix likely

38°F

29°F

Wind: 10 mph

Humidity: 100%

Total Precip: 0.76"

Attachments: 5



Apr 30, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Met with Casey and the drywall guy. Walked the site, identified areas still in need of nailers and/or demolition.

Talked with Ryan about the remaking had rough in and moving the upper level mop sink to match the changes made in the framing. Left @ 11am.

Returned @ 1:15p.

Documented fiber optic cable crew's work around our site.

Got the concrete and sonotube moved in front of the conex.

Locked up, powered down, and closed the site @ 2pm.

Weather Conditions:

Cloudy with slight chance of thunderstorms Thu, Apr 30, 2026, 7:23 AM

 Cloudy with slight chance of thunderstorms

43°F

33°F

Wind: 10 mph

Humidity: 99%

Total Precip: 1.28"

Attachments: 22



Apr 29, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Arrived at 8:15 am, set up, met with ownership team, re framed lower level door openings, demoed pony wall in 205, re framed doorway to restroom, framed up dividing wall between new bathroom entry and mop closet, infield old doorway to restroom, clean up, left site at 5pm

Weather Conditions:

Mostly cloudy with showers Wed, Apr 29, 2026, 5:06 PM

 Mostly cloudy with showers

52°F

Wind: 14 mph

37°F

Humidity: 91%

Total Precip: 0.23"

Attachments: 28



Apr 29, 2026

Job: 2927 W Pikes Peak Ave
Title: Ownership Team
Added By: Stephen Michaels

Log Notes:

Adjusted door openings to accommodate doors in conex.

Demoed upper level demising wall.

Relocated mop closet wall and doorway.

Cleaned up and left @ 3:30pm

Weather Conditions:

Cloudy with light wintry mix Wed, Apr 29, 2026, 2:07 PM



Cloudy with light wintry mix

50°F
33°F

Wind: 12 mph

Humidity: 95%

Total Precip: 0.25"

Attachments:

17



Apr 29, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up, removed steel plates, installed 2nd run of 6" water pipe. Talked with Adam (CSU) about iron spool piece needed inside riser room and wrap/sheath needed at wall penetration. 8" of clearance is needed to allow the fire system guys to do their work inside. Trevor said he'd pick that stuff up. Adam's sending him the details. As of 3:30pm neither Trevor nor myself have

heard anything from Adam.

Began forming inside abandoned storm drain in preparation for flow fill pour first thing tomorrow morning.

Weather Conditions:

Mostly cloudy with isolated storms Wed, Apr 29, 2026, 8:12 AM



Mostly cloudy with isolated storms

58°F

37°F

Wind: 11 mph

Humidity: 94%

Total Precip: 0.17"

Attachments: 18



Apr 29, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7:30am.

Unlocked, powered up, inspected, and opened the site.

Touched base with Trevor on his plan for the day.

Got things set up for concrete delivery.

Spot cleaned, labeled rooms in preparation for backing.

Retrieved ERV1 info for Caleb. Talked with Adam (CSU guy) about 6" water line penetration and what's required through the wall and on either side.

Began preparing plan/layout for backing.


Assisted Casey and Ownership team with upper level framing.
Locked up, powered down, and closed the site @ 5pm.

Weather Conditions:

Mostly cloudy with showers Wed, Apr 29, 2026, 7:50 AM

 Mostly cloudy with showers **57°F** Wind: 12 mph
38°F Humidity: 90%
Total Precip: 0.17"

Attachments: 10

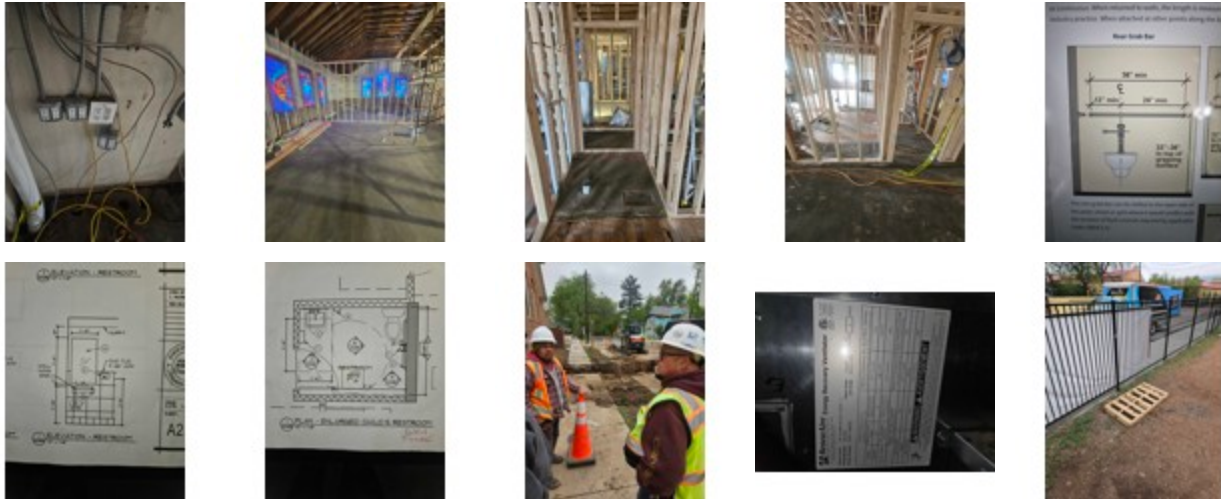

Apr 28, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Continued punching through wall for water line insertions. Punched through @ 1pm. Cleaned out hole.
Waited around for a 90°. Covered the sidewalk hole, cleaned, and left @ 4:45pm.

Weather Conditions:

Mostly cloudy with isolated storms Tue, Apr 28, 2026, 1:20 PM

 Mostly cloudy with isolated storms **57°F** Wind: 16 mph
35°F Humidity: 87%
Total Precip: 0.05"



Apr 28, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am.

Returned @ 11:45am.

Excavator crew was working on punching through the wall.

Exterior trash walk, plan/schedule study.

Locked up, powered down, put up caution tape around excavation site, and closed the site.

Left @ 4:45pm.

Weather Conditions:

Partly cloudy with showers Tue, Apr 28, 2026, 6:49 AM

 Partly cloudy with showers

57°F

34°F

Wind: 13 mph

Humidity: 96%

Total Precip: 0.06"



Apr 27, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Arrived @ 9am.

Set up. Removed steel panels from hole.

Cut rebar and removed rubble from abandoned storm drain. Installed one length of 6" water line. Began drilling through foundation. Installed curb stop valve.

Covered hole back up with steel panels and left around 6:30pm.

Weather Conditions:

Partly cloudy with isolated storms Mon, Apr 27, 2026, 10:32 AM



Partly cloudy with isolated storms

60°F

40°F

Wind: 9 mph

Humidity: 79%

Total Precip: 0.19"



Apr 27, 2026

Job: 2927 W Pikes Peak Ave

Title: Iron Mountain (Lav)

Added By: Stephen Michaels

Log Notes:

Arrived @ 9am.

Serviced lav and moved it inside the rear gate/fence to try and keep out the riff raff.

Left @ 9:15am

Weather Conditions:

Partly cloudy with isolated storms Mon, Apr 27, 2026, 10:32 AM



Partly cloudy with isolated storms

60°F

40°F

Wind: 9 mph

Humidity: 79%

Total Precip: 0.19"

Attachments: 1



Apr 27, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up. Ran thermostat wire. Looked through plans and discussed necessary revisions.

Left @ 3pm.

Weather Conditions:

Partly cloudy with isolated showers Mon, Apr 27, 2026, 7:02 AM



Partly cloudy with isolated showers

61°F

Wind: 18 mph

38°F

Humidity: 79%

Total Precip: 0.18"

Attachments: 2



Apr 27, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Discussed moving the porta lav inside the fence with the Iron Mountain technician. We moved it just inside the back gate.

Schedule/plan study. Exterior trash walk.

Left @ 12:30pm to pick up plans.

Returned @ 1pm.

Supervised city water tap work.

Locked up, powered down, and closed the site @ 5pm.

Weather Conditions:

Partly cloudy with isolated showers Mon, Apr 27, 2026, 7:02 AM

Wind: 18 mph

 Partly cloudy with isolated showers

61°F
38°F

Humidity: 79%
Total Precip: 0.18"

Attachments: 11



Apr 24, 2026

Job: 2927 W Pikes Peak Ave
Title: PPRBD (Electrical Rough Inspection)
Added By: Stephen Michaels
Log Notes:
Passed
Weather Conditions:
Mostly sunny Fri, Apr 24, 2026, 2:59 PM

 Mostly sunny

68°F
38°F

Wind: 18 mph
Humidity: 37%
Total Precip: 0"

Attachments: 1



Apr 24, 2026

Job: 2927 W Pikes Peak Ave
Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Arrived @ 7:15am.

Set up. Dug some to prepare to run water to the building. Sat around and waited for someone to hear from Trevor.

Uncovered some unmarked pipes. The crew is exposing them while waiting to hear back what they are.

We were told they are abandoned, but treat them like they're live.

Trevor said he will return with steel plates to cover the opening.

He returned and covered almost the whole hole with steel plates. He was short one. We heavily coned the area off, put up sidewalk closed signs, and wrapped it all with caution tape.

They left @ 6:15pm

Weather Conditions:

Mostly sunny Fri, Apr 24, 2026, 7:09 AM



Mostly sunny


71°F

34°F

Wind: 16 mph

Humidity: 43%

Total Precip: 0"

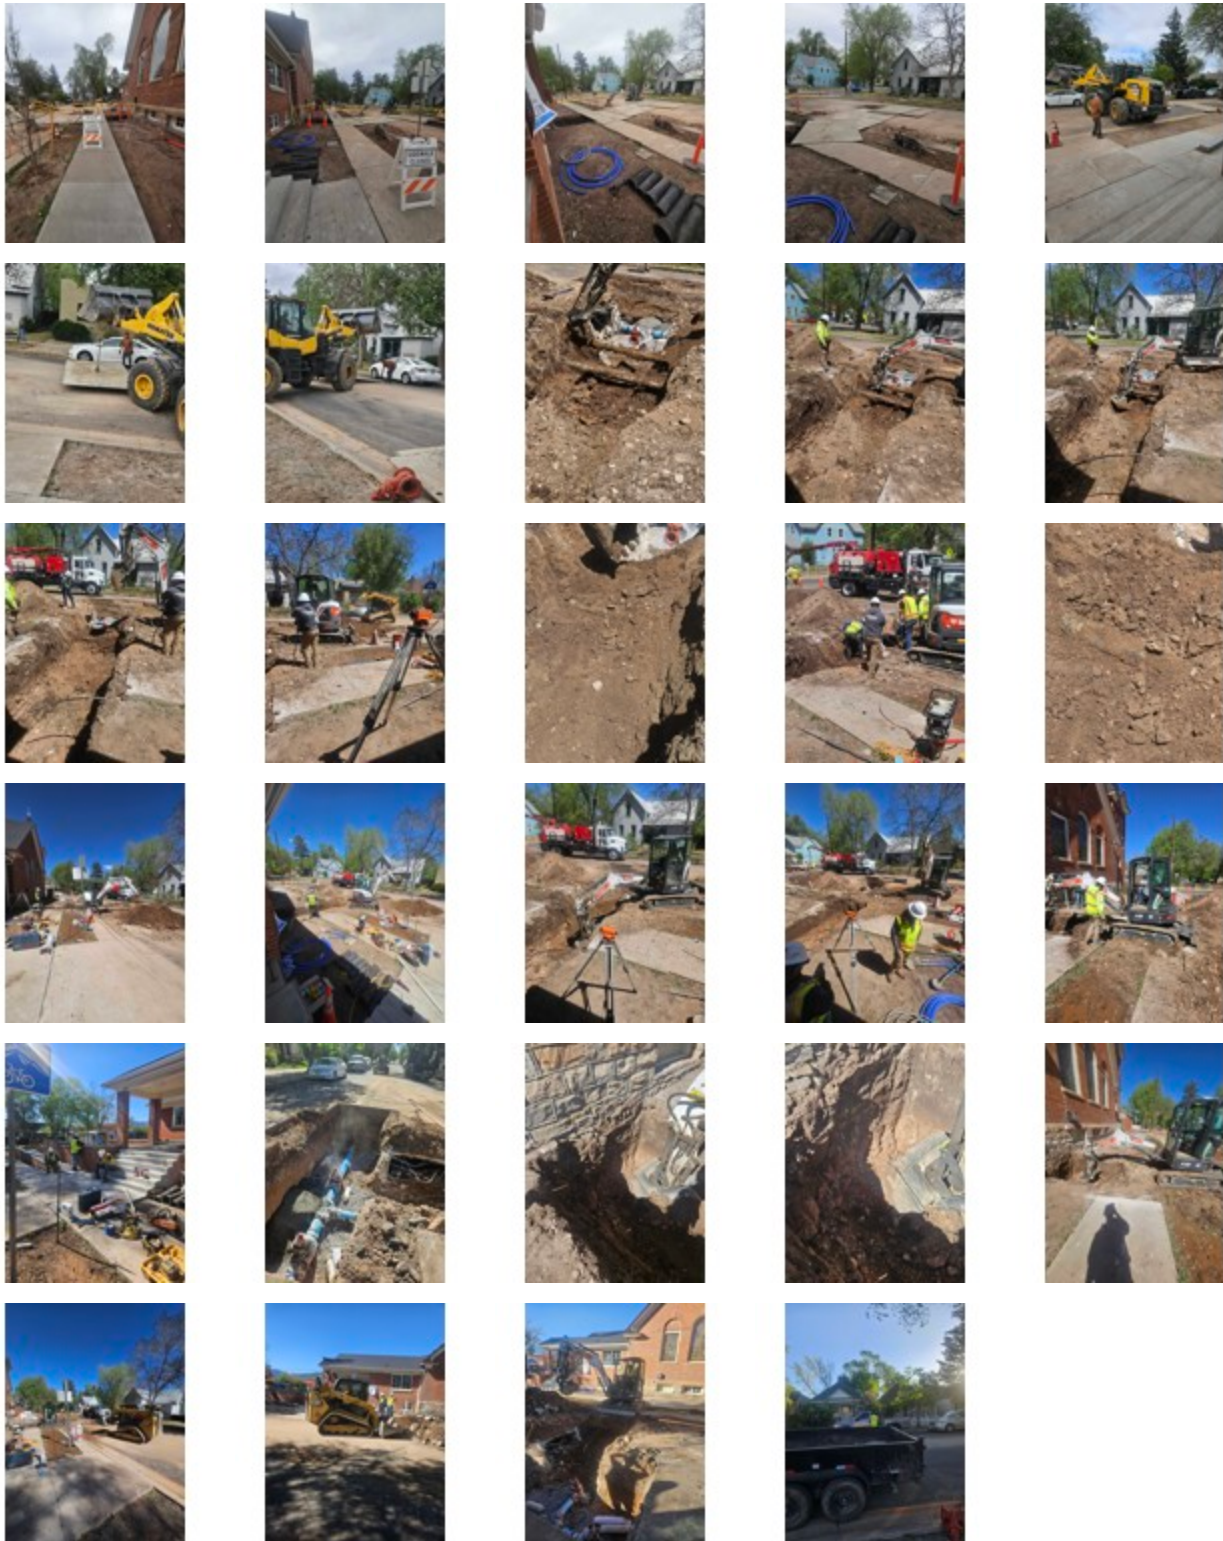

Apr 24, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Spoke with excavator about plan for the day. He kept digging.

Called Gustavo to update him concerning the playground area and the water tap for irrigation.

Uncovered two more unmarked pipes. Called Trevor to see what he knew he said he was dealing with it and would call me back.

811 came out and told us the pipes were abandoned, but we should treat them like they're live. Trevor told me that the city storm drain guy (Hank or Hal, I can't recall at the moment) told him that they need to put forms in the abandoned storm drain 10' in on both sides, then pump it in with flow fill. I taped to the city guy and he said that that is what he told Trevor. I told him 10' was an awful lot. He replied that we could put the forms in at 5'. I told him I just needed to know what was expected so that we can make a plan, if it needs to be 10' so be it, I just need to know. The city storm drain guy said that 5' was fine. I asked him if there was a code that dictated that we fill, for example, 2' past the cut that was made. He said no, but we were the ones that demolished it. I told him we had our locates done and had a representative of the city (Adam with CSU) on site that told the excavators to start drilling into it. He told me it didn't belong to CSU, that it was city property. I asked again if there was a hard and fast rule about how this is dealt with and he either didn't know, or didn't want to tell me.

Installed caution tape around the hole.

Locked up, powered down, and closed the site @ 4:30pm.

Returned @ 5:15pm.

Supervised placement of steel plates over open hole. They were short one steel plate. I called Casey about it and he said it's not good, but if that's all they have it is what it is, and try to make it safe as possible. We heavily coned the area off, put up sidewalk closed signs, and wrapped it all with caution tape.

I left a 6:30pm.

Weather Conditions:

Mostly sunny Fri, Apr 24, 2026, 7:09 AM



Mostly sunny

71°F

34°F

Wind: 16 mph

Humidity: 43%

Total Precip: 0"



Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: PPRBD Elec. Inspection

Added By: Marlowe Downey

Log Notes:

Arrived at 1:00

-Inspected lower level electrical rough (passed)

-Will be coming back tomorrow for upper level inspection

Left at 1:15

Weather Conditions:

Mostly sunny Thu, Apr 23, 2026, 1:09 PM



63°F

42°F

Wind: 23 mph

Humidity: 32%

Total Precip: 0"

Attachments: 4



Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorp Excavation

Added By: Marlowe Downey

Log Notes:

Arrived at 7:15

-Started on pipe assembly

-Site planning

-Cut the street (I informed workers to use water to midi-gate dust)

-Cut the side walk

-Currently demoing cut road

- Casey spoke with Trevor

CSU changed their piping requirements due to the size and type of existing piping, Trevor changed the tap to assembly to new required specs with threaded taps in leu of the saddle taps as previously on site, their plan is to complete the road work portion including asphalt and be out of the roadway by end of day tomorrow/ 4/24 and finish the remaining work from the curb stop into the building over the next few days, once they complete the work they will schedule the hydrostatic and flow and flush tests with CSFD and CSU, then we can schedule the fire sprinkler and plumbers back in to complete their work,

-He also plans to complete the parking approach work next week

-Ran into abandoned drainage system

-Started demo with approval from Colorado Springs Utility inspector

Weather Conditions:

Mostly sunny Thu, Apr 23, 2026, 8:53 AM



63°F

43°F

Wind: 16 mph

Humidity: 30%

Total Precip: 0"





Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived 7:24

-Supervising CWAM

-Supervising the city tap

Weather Conditions:

Mostly sunny Thu, Apr 23, 2026, 7:24 AM



63°F

43°F

Wind: 16 mph

Humidity: 30%

Total Precip: 0"

Attachments: 0

Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Scheduling, supervision, oversight,

Arrived at 9:30, met with mechanical crew and excavators and CSU pipeline inspector, the excavators will have the excavation done as well as both taps completed by 3pm, they will set the couplings in concrete to cure overnight, they will steal plate the open hole for the night, left site at 10:05,

Spoke with Trevor on the phone at 1:30 pm, CSU changed their piping requirements due to the size and type of existing piping, Trevor changed the tap to assembly to new required specs with threaded taps in leu of the saddle taps as previously on site, their plan is to complete the road work portion including asphalt and be out of the roadway by end of day tomorrow/ 4/24 and finish the remaining work from the curb stop into the building over the next few days, once they complete the work they will schedule the hydrostatic and flow and flush tests with CSFD and CSU, then we can schedule the fire sprinkler and plumbers back in to complete their work, he also plans to complete the parking approach work next week,

Attachments: 4



Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Thorpe Excavation

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up for city tap.

The crew came upon a 7' wide concrete block buried about 8 inches under the asphalt. We weren't sure what it was so I sent pictures to Casey and Caleb, who made some calls to figure out what it was. While that was occurring, I heard them begin jack hammering, I came to see what was going on and Adam (CSU guy) was pointing out to the excavator where to drill. When I asked the excavator who told him to go ahead and drill, he said that Ayan had. Adam informed me that it may be a storm drain, in which case it'll have to be replaced. He said he spoke to Trevor and told him to call and make sure what the tunnel was. Caleb showed up on site to check things out. Adam then checked his data base and said that his system isn't showing any storm drains in this area.

Weather Conditions:

Mostly sunny Thu, Apr 23, 2026, 7:38 AM

 Mostly sunny
63°F
43°F
Wind: 16 mph
Humidity: 30%
Total Precip: 0"

Attachments: 13



Apr 23, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable Solutions (HVAC)

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

-Set up job site

-Tapped copper lines in lower level and exterior units

Attachments: 2



Apr 23, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Began organizing excess material for Caleb's count.

Left @ 7:45am.

Returned @ 2pm.

Observed and supervised excavation work. The crew came upon a 7' wide concrete block buried about 8 inches under the asphalt. We weren't sure what it was so I sent pictures to Casey and Caleb, who made some calls to figure out what it was. While that was occurring, I heard them begin jack hammering, I came to see what was going on and Adam (CSU guy) was pointing out to the excavator where to drill. When I asked the excavator who told him to go ahead and drill, he said that Ayan had. Adam informed me that it may be a storm drain, in which case it'll have to be replaced. He said he spoke to Trevor and told him to call and make sure what the tunnel was. Caleb showed up on site to check things out. Adam then checked his data base and said that his system isn't showing any storm drains in this area.

Locked up, powered down, and closed the site @ 4:30pm.

Weather Conditions:

Mostly sunny Thu, Apr 23, 2026, 6:55 AM



Mostly sunny

63°F

43°F

Wind: 16 mph

Humidity: 30%

Total Precip: 0"

Attachments: 13



Apr 22, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 2:52

-Turned off all lights

-Insured all windows shut

-Locked lower level door and insured all doors were locked

-Preformed a perimeter sweep (found nothing unusual)

Left at 2:55

Weather Conditions:

Mostly sunny Wed, Apr 22, 2026, 2:53 PM



77°F

49°F

Wind: 23 mph

Humidity: 40%

Total Precip: 0"

Attachments: 0

Apr 22, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 6:45am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:15am.

Returned @ 3:45pm.

Retrieved lav lock, inspected the site, locked up repaired lav, and left @ 4pm.

Weather Conditions:

Partly cloudy with patchy blowing dust Wed, Apr 22, 2026, 6:51 AM



Partly cloudy with patchy blowing dust

78°F

47°F

Wind: 22 mph

Humidity: 39%

Total Precip: 0"

Attachments: 1



Apr 21, 2026

Job: 2927 W Pikes Peak Ave

Title: Casey Copley Supervision

Added By: Casey Copley

Log Notes:

Steve opened site, scheduling, pm work, spoke with the Luke and Kelly, spoke with the engineer and we should have the requested mechanical and electrical revisions tomorrow, also gave approval for the isometric gas drawings,,

Weather Conditions:

Mostly sunny Tue, Apr 21, 2026, 2:06 PM



Mostly sunny

79°F

48°F

Wind: 13 mph

Humidity: 25%

Total Precip: 0"

Attachments: 0

Apr 21, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7:30am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:45am

Weather Conditions:

Mostly sunny Tue, Apr 21, 2026, 10:19 AM



Mostly sunny

78°F

48°F

Wind: 12 mph

Humidity: 25%

Total Precip: 0"

Attachments: 0

Apr 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Marlowe
Added By: Marlowe Downey

Log Notes:

Arrived at 4:20

- Took over supervision of the framers from Casey
- Swept up and organized
- Locked job box
- Turned off lights and made sure all windows are closed and locked
- Locked door and insured the rest were locked

4:56

Weather Conditions:

Partly cloudy Mon, Apr 20, 2026, 4:48 PM



77°F
40°F

Wind: 12 mph
Humidity: 19%
Total Precip: 0"

Attachments: 3



Apr 20, 2026

Job: 2927 W Pikes Peak Ave
Title: American electrician
Added By: Casey Copley

Log Notes:

Installed lighting in lower level hallway, installed boxes for exit signs and frog eyes,

Weather Conditions:

Mostly sunny Mon, Apr 20, 2026, 12:00 AM



75°F
42°F

Wind: 14 mph
Humidity: 26%
Total Precip: 0"

Attachments: 9



Apr 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Pursuit of excellence framing
Added By: Casey Copley
Log Notes:

Arrived at 8 am, set up, finished doorway framing, finished wall firing, framed around fire panel, clean up, left at 4pm

Weather Conditions:

Mostly sunny Mon, Apr 20, 2026, 12:00 AM



75°F
42°F

Wind: 14 mph
Humidity: 26%
Total Precip: 0"

Attachments: 6



Apr 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley
Log Notes:

Steve opened site, supervision, scheduling, cleaning, verifications on framing and electrical

Weather Conditions:

Mostly sunny Mon, Apr 20, 2026, 12:00 AM



75°F
42°F

Wind: 14 mph
Humidity: 26%
Total Precip: 0"

Attachments: 3



Apr 20, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:30am.

Weather Conditions:

Partly cloudy Mon, Apr 20, 2026, 6:47 AM



Partly cloudy

75°F
40°F

Wind: 10 mph
Humidity: 22%
Total Precip: 0"

Attachments: 2



Apr 17, 2026

Job: 2927 W Pikes Peak Ave
Title: Casey Copley Supervision
Added By: Casey Copley

Log Notes:

Steve opened site, met with framing crew and lined them out on remaining scope, supervision, scheduling, pm work, site inspection, closed site at 4:15 pm

Weather Conditions:

Partly cloudy with snow Fri, Apr 17, 2026, 3:32 PM



Partly cloudy with snow

57°F

Wind: 24 mph
Humidity: 91%

26°F Total Precip: 0.2"

Attachments: 4



Apr 17, 2026

Job: 2927 W Pikes Peak Ave
Title: Pursuit of excellence Framing
Added By: Casey Copley

Log Notes:

Arrived at 8 am, unloaded, set up, framed lower level hallway soffit, framed in upper level door and hall opening in classroom 204, unfilled floor, removal of temp walls, clean up, left site at 4 pm

Weather Conditions:

Partly cloudy with snow Fri, Apr 17, 2026, 3:32 PM



Partly cloudy with snow


57°F

Wind: 24 mph

26°F

Humidity: 91%

Total Precip: 0.2"

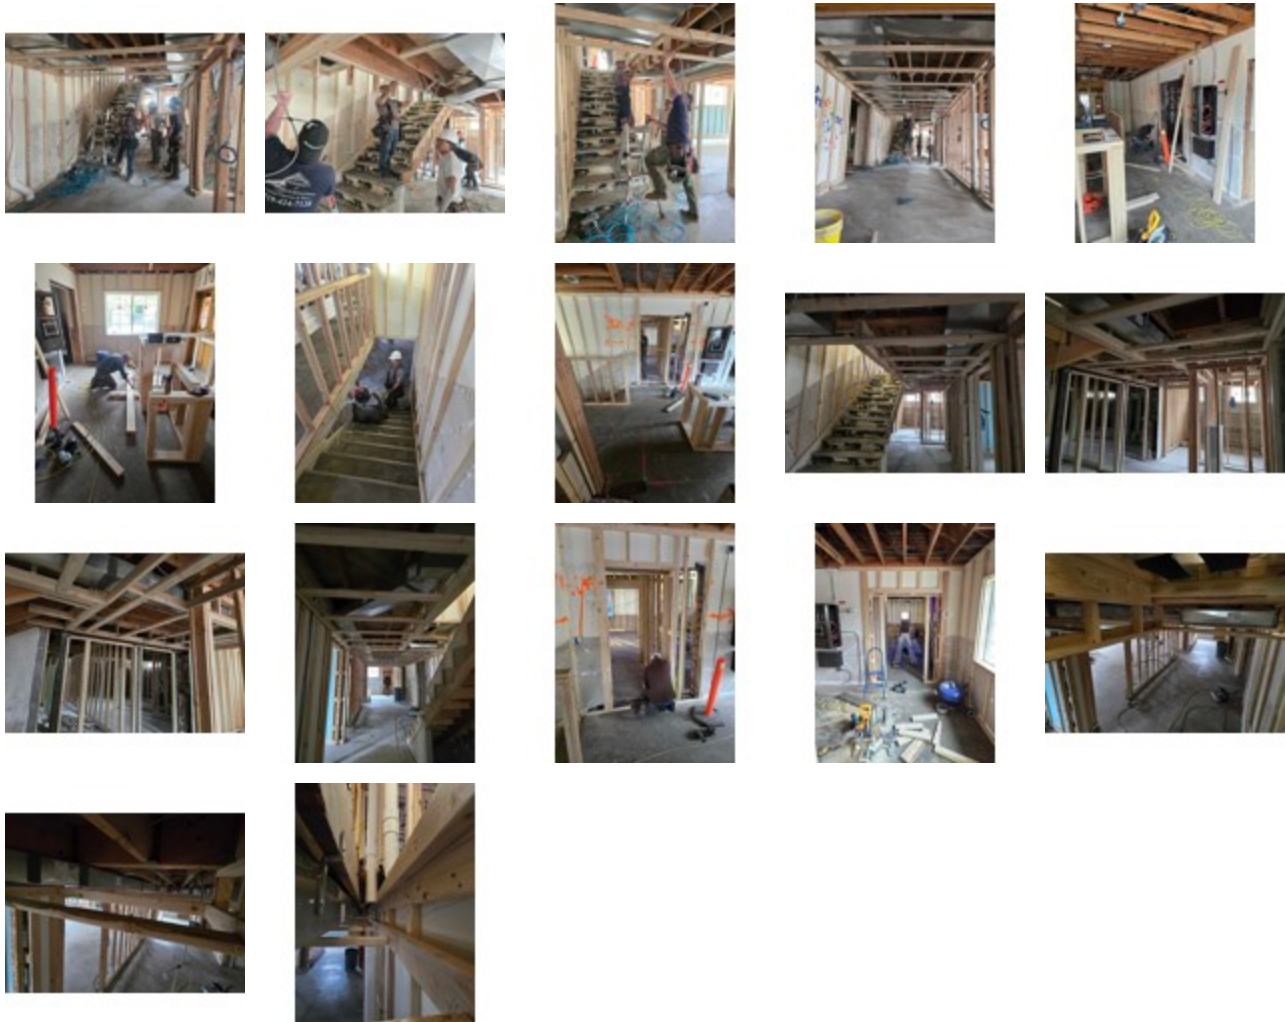

Apr 17, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Casey arrived @ 8am. I touched base with him for a bit, discussed some of the plans for the day.

Left @ 8:15am.

Weather Conditions:

Partly cloudy with light wintry mix Fri, Apr 17, 2026, 7:16 AM



Partly cloudy with light wintry mix

57°F
29°F

Wind: 24 mph

Humidity: 70%

Total Precip: 0.11"

Attachments: 1



Apr 16, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Set up and continued installing lower level ducts and preparing to pressure test hole heads. Pressure test is good, everything's holding, no leaks.

Finished lower level stub-ins.

Adjusted and installed vertical ducting in upper level chase.

Cleaned up and left @ 4pm.

Weather Conditions:

Mostly sunny Thu, Apr 16, 2026, 7:45 AM



Mostly sunny

75°F

43°F

Wind: 21 mph

Humidity: 37%

Total Precip: 0"

Attachments: 10



Apr 16, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Exterior trash walk and leaf blowing.

Left @ 8am.

Returned @ 10:30am.

Discovered lock bracket torn off of the porta potty again. Called Iron Mountain and left a message.

Weather Conditions:

Mostly sunny Thu, Apr 16, 2026, 6:45 AM

 Mostly sunny **75°F**
39°F Wind: 21 mph
Humidity: 47%
Total Precip: 0"

Attachments: 3



Apr 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Rock N Roll-offs

Added By: Stephen Michaels

Log Notes:

Arrived @ 7 and swapped out the dumpster.

Weather Conditions:

Mostly sunny Wed, Apr 15, 2026, 6:42 AM

 Mostly sunny **59°F**
29°F Wind: 10 mph
Humidity: 65%
Total Precip: 0"

Attachments: 2



Apr 15, 2026

Job: 2927 W Pikes Peak Ave

Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, and opened the site.

HVAC was here for, like, 5 minutes, but they left.

Locked up and left @ 7:30am

Weather Conditions:

Mostly sunny Wed, Apr 15, 2026, 6:42 AM



Mostly sunny

59°F

29°F

Wind: 10 mph

Humidity: 65%

Total Precip: 0"

Attachments: 2



Apr 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up and continued fabricating and installing ducting, moving from the lower level through to the upper.

Also continued fabrication and install of lower level ducting.

Cleaned up and left @ 3:15pm

Weather Conditions:

Partly cloudy with showers Tue, Apr 14, 2026, 7:26 AM



Partly cloudy with showers

63°F

42°F

Wind: 17 mph

Humidity: 54%

Total Precip: 0"

Attachments: 10



Apr 14, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Supervised HVAC work. Schedule/plan study.

Emptied trash cans/buckets. Called Dan (Dumpster guy) and let him know our dumpster's full. He said he'll swing by in the morning and switch us out.

CSU locates guy came out and marked everything out.

Left @ 12:30pm.

Returned @ 1:45pm.

Exterior trash walk and leaf blow.

Locked up, powered down, and closed the site @ 4pm.

Weather Conditions:

Partly cloudy with showers Tue, Apr 14, 2026, 6:56 AM



Partly cloudy with showers

63°F

42°F

Wind: 17 mph

Humidity: 54%

Total Precip: 0"

Attachments: 8



Apr 13, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 9:00

-delivered 5 sheets of 4'x8' 1/2" drywall (stacked left side of lower level entry door)

Left at 9:10

Weather Conditions:

Mostly sunny Mon, Apr 13, 2026, 9:09 AM



74°F

48°F

Wind: 21 mph

Humidity: 33%

Total Precip: 0"

Attachments: 1



Apr 13, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up to continue fabricating and installing lower level ducting.

Weather Conditions:

Mostly sunny Mon, Apr 13, 2026, 6:39 AM



Mostly sunny

69°F

Wind: 17 mph

37°F

Humidity: 93%

Total Precip: 0"

Attachments: 1

Apr 13, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Left @ 7:45.

Returned @ 9am.

Was going to hang drywall for HVAC but that turned out to be unnecessary.

Left @ 9:45am.

Returned @ 1am.

Spoke with Mike about a few questions. Was then informed by Casey that Caleb was on his way. Marlowe and I loaded unnecessary drywall back in his truck to return.

Left @ 2pm.

Weather Conditions:

Mostly sunny Mon, Apr 13, 2026, 6:39 AM



Mostly sunny

69°F

37°F

Wind: 17 mph

Humidity: 93%

Total Precip: 0"

Attachments:

0

Apr 10, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Opened the site and continued fabricating and installing ducting in lower level.

Cleaned up and left @ 3:15pm.

Weather Conditions:

Partly cloudy with showers Fri, Apr 10, 2026, 7:33 AM



Partly cloudy with showers

61°F

42°F

Wind: 18 mph

Humidity: 86%

Total Precip: 0.01"

Attachments:

14



Apr 10, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

HVAC was already on site. I hung danger signs from the caution tape between the demarcation poles, inspected the site, and

left @ 7:45am.

Returned @ 12am.

HVAC still working on lower level ducting.

Scheduling, plan study, safety research, supervision.

Locked up, powered down, and closed the site @ 3:30pm.

Weather Conditions:

Partly cloudy with showers Fri, Apr 10, 2026, 7:33 AM



Partly cloudy with showers

61°F

42°F

Wind: 18 mph

Humidity: 86%

Total Precip: 0.01"

Attachments: 1

Apr 9, 2026

Job: 2927 W Pikes Peak Ave

Title: Affordable Solutions (HVAC)

Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Set up and continued fabricating and installing ducting for lower level.

Left for employee reviews @ 12pm. Not sure if/when they will return.

Weather Conditions:

Partly cloudy with showers Thu, Apr 9, 2026, 7:30 AM



Partly cloudy with showers

71°F

39°F

Wind: 8 mph

Humidity: 71%

Total Precip: 0.01"

Attachments: 8



Apr 9, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Met with Caleb and Mike to discuss what HVAC work can continue while the rest gets worked out.

Cut Radon pipes to make room for 36"×6" ducting in lower level.

Left @ 7:45am.

Returned @ 9am.

Cut some more radon piping that the Mech guys needed out of their way.

Plan/schedule study. Trash walk, area beautification.

Locked up, powered down, and closed the site @ 12:15pm.

Returned @ 2pm.

Set up cones and caution tape at the upper level back door as there is a fall hazard. Spoke with Cody and he will make up some danger signs for me on the morning.

Job board/safety study.

Locked up again and left @ 3:45pm

Weather Conditions:

Partly cloudy with showers Thu, Apr 9, 2026, 6:46 AM



Partly cloudy with showers

70°F
38°F

Wind: 9 mph

Humidity: 75%

Total Precip: 0.03"

Attachments: 8



Apr 8, 2026

Job: 2927 W Pikes Peak Ave
Title: American Electrician
Added By: Stephen Michaels

Log Notes:

Arrived @ 8am.

Set up. Continued running power to exterior lights and exit signs.

Organized Connex.
Cleaned up and left @ 2:45pm.

Weather Conditions:

Partly cloudy with showers Wed, Apr 8, 2026, 8:44 AM



Partly cloudy with showers

72°F

41°F

Wind: 8 mph

Humidity: 55%

Total Precip: 0"

Attachments: 4



Apr 8, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels

Log Notes:

Arrived @ 7:45am.
Unlocked, powered up, inspected, and opened the site.
Ran to Ace @ 9am.
Returned @ 9:30am.
Perimeter trash walk and blew out the parking lot.
Schedule/plan study. Job board study.
Left to help Marlowe @ 1:30pm.

Returned to secure site @ 2:45pm
Locked up, powered down, and closed the site @ 3pm.

Weather Conditions:

Partly cloudy with showers Wed, Apr 8, 2026, 7:43 AM



Partly cloudy with showers

65°F

38°F

Wind: 8 mph

Humidity: 55%

Total Precip: 0"

Attachments: 1



Apr 7, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision

Added By: Stephen Michaels

Log Notes:

Arrived @ 2pm.

Ben and John were just finishing up an NPR interview. I was told the electricians were here today, but I didn't see them.

Cleaned and organized the site.

Locked up, powered down, and closed the site @ 3pm.

Weather Conditions:

Partly cloudy with showers Tue, Apr 7, 2026, 1:42 PM



Partly cloudy with showers

65°F

34°F

Wind: 14 mph

Humidity: 76%

Total Precip: 0.02"

Attachments: 0

Apr 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Dropped off tools from 1802 so they don't get stolen from bed of truck.

-Returned tools

Weather Conditions:

Partly cloudy with showers Mon, Apr 6, 2026, 4:11 PM



72°F

40°F

Wind: 12 mph

Humidity: 49%

Total Precip: 0"

Attachments: 2



Apr 6, 2026

Job: 2927 W Pikes Peak Ave

Title: Engineer/HVAC Design Meeting

Added By: Stephen Michaels

Log Notes:

Everyone showed up around 9:45am

Lowell and Bryan walked the site with Shane, HVAC Mike, Caleb, and myself.

Duct routing problems were identified, and Solutions were worked through.

Meeting wrapped and everyone headed their seperated ways around 11am.

Weather Conditions:

Partly cloudy with showers Mon, Apr 6, 2026, 12:56 PM

Wind: 11 mph

 Partly cloudy with showers

68°F
38°F

Humidity: 42%
Total Precip: 0"

Attachments: 14



Apr 6, 2026

Job: 2927 W Pikes Peak Ave
Title: Pursuit of Excellence Framing
Added By: Stephen Michaels

Log Notes:

Arrived @ 8:15am.

Pino and Nick walked the site and discussed today's score of work with me. They're pulling that lower level soffit to make room for the HVAC work and framing lower level door frames. They are holding off on dropping the ceiling until HVAC's work is done to prevent having to undo/redo work.

Nick began framing lower level door frames.

Cleaned up and left @ 4:45pm.

Weather Conditions:

Partly cloudy with showers Mon, Apr 6, 2026, 8:55 AM

 Partly cloudy with showers

70°F
39°F

Wind: 11 mph
Humidity: 43%
Total Precip: 0"



Apr 6, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Mike walked the site to plan out the day's work scope and went over a couple concerns with me including the Radon system being in the way, and the soffit by the lower level back door not being wide enough to for his ducting.

Engineer design meeting @ 9:45am.

Left between 12pm and 2pm.

Weather Conditions:

Partly cloudy with showers Mon, Apr 6, 2026, 8:55 AM

 Partly cloudy with showers

70°F
39°F

Wind: 11 mph
Humidity: 43%
Total Precip: 0"



Apr 6, 2026

Job: 2927 W Pikes Peak Ave
Title: Steve Michaels Supervision
Added By: Stephen Michaels
Log Notes:

Arrived @ 7am.

Unlocked, powered up, inspected, and opened the site.

Blew off sidewalks.

Walked site with HVAC Mike, Pino, and Nick. Discussed scope of work and identified problem areas.

Walked jobsite with Caleb, Lowell, Bryan, Shane, and HVAC Mike; identified duct routing conflicts and possible solutions.

Left @ 11:30am.

Returned @ 2pm.

HVAC guys had left at some point when I was @ the other site.

Nick continues to frame door openings.

Left @ 2:30pm.

Returned @ 4pm.

Locked up, powered down, and closed site @ 4:45pm.

Weather Conditions:

Partly cloudy with showers Mon, Apr 6, 2026, 6:40 AM



Partly cloudy with showers

69°F

34°F

Wind: 12 mph

Humidity: 92%

Total Precip: 0"

Attachments: 9



Apr 3, 2026

Job: 2927 W Pikes Peak Ave

Title: Marlowe

Added By: Marlowe Downey

Log Notes:

Arrived at 7:10

- Swept upper and lower level rooms that required attention
- Picked up cups and trash left by others with Steve
- Shortly supervised the plumbers and CWAM

Left at 7:45

Weather Conditions:

Mostly sunny Fri, Apr 3, 2026, 8:04 AM



54°F

38°F

Wind: 21 mph

Humidity: 60%

Total Precip: 0"

Attachments: 0

Apr 3, 2026

Job: 2927 W Pikes Peak Ave

Title: CSU Plumbing Rough Inspection

Added By: Stephen Michaels

Log Notes:

Passed.

Arrived @ 9:15.

Checked yesterday's issues for correction, liked what he saw.

Left @ 9:30am.

Weather Conditions:

Mostly sunny Fri, Apr 3, 2026, 9:30 AM



Mostly sunny

54°F

34°F

Wind: 17 mph

Humidity: 68%

Total Precip: 0"

Attachments: 4



Apr 3, 2026

Job: 2927 W Pikes Peak Ave
Title: Affordable Solutions (HVAC)
Added By: Stephen Michaels

Log Notes:

Arrived @ 7am.

Continued fabricating and installing ducts.

Cleaned up and left @ 12pm.

Weather Conditions:

Mostly sunny Fri, Apr 3, 2026, 7:03 AM

 Mostly sunny
54°F Wind: 17 mph
34°F Humidity: 68%
Total Precip: 0"

Attachments: 6

